



DMCI Homes

Account Management & Reporting Phase 1 MVP (T&M) Labo Proposal

BJIT Ltd.
BJIT Singapore Pte. Ltd.
2026/02/18 version.1.0.0

YOUR NEXT DESTINATION
OF SOFTWARE OUTSOURCING

Version History

Doc. Ver.	Author (Date)	Reviewer (Date)	Approver (Date)	Remarks
1.0.0	BJIT Estimation & Proposal team 18.02.2026	BJIT Estimation & Proposal team 18.02.2026	Abul Kalam 18.02.2026	DMCI Account Management Reporting - Phase 1 MVP Proposal

Document Classification

This document has been classified as **CONFIDENTIAL** document as per BJIT's Information Security Management System and can only be shared with the following members / teams:

- ❖ DMCI Homes. – respective stakeholders
- ❖ BJIT respective stakeholders and members assigned for this project

Executive Summary (1 of 2)



Business Context:

DMCI currently generates the Buyer's subsidiary ledger (BSL) report through a manual Excel-based process using data extracted from Dynamics 365. The report plays a critical role in evaluating customer account performance, revenue recognition, contract asset positions, and overall financial exposure.

As data volume and reporting complexity increase, the existing manual approach presents operational limitations and control risks.

Current Challenges:

- Manual consolidation and formula-driven Excel computations
- High dependency on specific personnel
- Risk of calculation inconsistencies and human error
- Limited scalability for growing data volume
- Longer report preparation cycle
- Restricted ability for secure, role-based report access

Executive Summary (2 of 2)

Proposed Solution:

BJIT proposes an automated Account Management & Reporting solution using Microsoft Azure and Power BI.

- Automate data extraction from Dynamics 365 (All Property Units, CWT, BSL)
- Integrate controlled manual adjustment files
- Centralize financial computations within an auditable ETL framework
- Replicate existing business logic with minimum reconciliation tolerance
- Deliver secure, project-based dashboards through Power BI

Key Benefits:

- Elimination of manual Excel-based reporting
- Improved financial accuracy and auditability
- Reduced operational risk
- Faster monthly reporting cycle (< 2 hours ETL processing)
- Secure Row-Level Security (RLS) for project managers
- Scalable platform for future reporting expansion

Expected Outcome:

Upon completion, DMCI will have a centralized, automated, and scalable financial reporting platform that enhances governance, improves efficiency, and supports data-driven decision-making across the organization.

Proposal Background

- BJIT and DMCI are collaborating on the implementation of the Account Management & Reporting solution using an Agile, Time & Material-based delivery model
- The same Agile methodology, governance structure, and team collaboration approach currently adopted in other BJIT-DMCI initiatives will be applied to ensure continuity and consistency
- The overall objectives and high-level feature areas (ETL automation, financial logic implementation, and reporting dashboards) are defined at a strategic level
- Detailed requirements, calculation refinements, and reporting enhancements will be iteratively refined through structured sprint planning sessions
- For each sprint:
 - DMCI provides a prioritized sprint backlog
 - BJIT estimates effort and commits work based on agreed resource bandwidth
 - Development and validation are executed incrementally with continuous stakeholder feedback
- T&M-based model enables flexible scope evolution, transparent effort tracking, and phased delivery aligned with future roadmap expansion



Current Process (1 of 2)

To fulfill the data requirements for completing the BSL report, the Accounting department extracts data from **Microsoft Dynamics AX**. Three raw data reports are generated from the system:

- **Buyers Subsidiary Ledger (BSL)** – A ledger containing all customer accounts related to property purchases.
- **Creditable Withholding Tax (CWT)** – Records of payments made in relation to customers' properties.
- **Property Management** – Provides contract price details for each customer account.

Currently, the only way to complete the BSL report is by extracting these reports from Dynamics AX, importing the data into Microsoft Excel, and manually adding calculated and formulated columns within Excel.

For details on how the data extraction is performed, please refer to the Microsoft Dynamics AX screenshot on next slide.

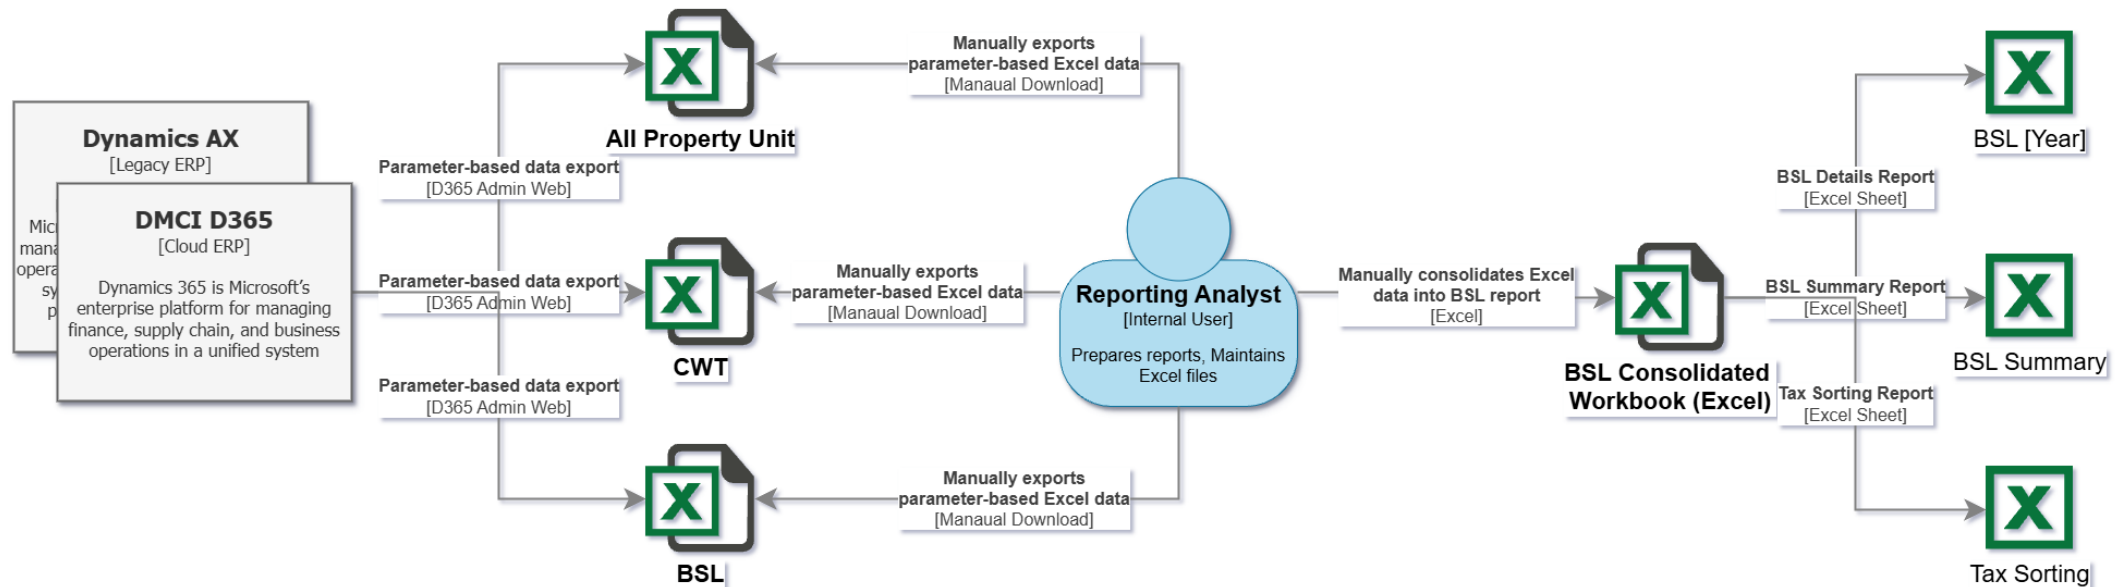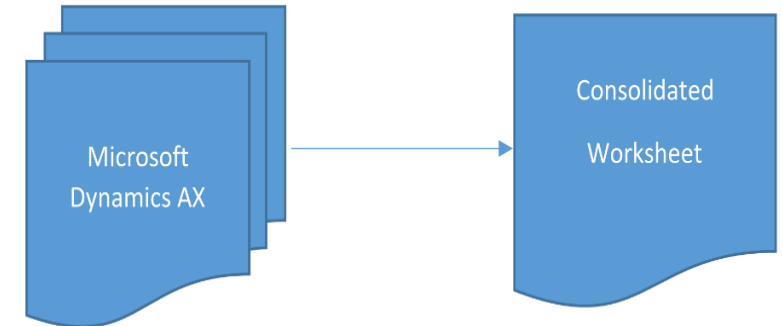

Current Process (2 of 2)

Microsoft Dynamics AX screenshot



DMCI HOMES
Feels real good to be home

On the day of closing of books

• Extra

Microsoft Dynamics AX - DMCI Project Developers Incorporated [DMCIAOSP06: Session ID - 14901] - [1 - dpdi - initial]

DPDI > Property management > Inquiries

4. One project at a time only unlike All Property units and CMT Masterfile that can

4. Cutoff: Actual date of extraction

On the day of closing of books

• Extra

Microsoft Dynamics AX (1)

Billing schedule

Contract number:

Billing schedule number:

Select

OK Cancel

Select the query to be edited.

IgnBillingScheduleInquiry (1 - dpdi)

Select query: **Previously used query** Modify...

Table

Billing schedule

Range Sorting

Table	Derived table	Field	Criteria
Billing schedule	Billing sched...	Contract number	sc-*
Billing schedule	Billing sched...	Billing schedule type	TCP
Billing schedule	Billing sched...	Status	Active

Add Remove

Reset OK Cancel

Current Challenges




Challenges:

- Manual data entry is required because the data originates from three different sources.
- Whenever there is a data update (e.g., changes in VAT), the team must recreate columns, revise formulas, and reapply all related changes. This process is time-consuming and inefficient.
- As data volume increases, Microsoft Excel is no longer able to handle the heavy calculations required for the report efficiently.
- The BSL report alone consumes a significant amount of computer processing resources, impacting overall system performance.
- Developers require clear data mapping from **Microsoft Dynamics AX** to accurately design and generate the required BSL reports.

		OK 01.12.23	OK 01.12.23	OK 12.22.23	OK 01.12.24	OK 01.12.24	OK 01.12.24	OK 01.12.24	OK 01.12.24	OK 01.12.24	OK 01.12.24	OK 01.12.24	OK 01.12.24	OK 01.12.24	OK 01.12.24	OK 01.12.24	OK 01.12.24	OK 01.12.24
BUYER'S SUBSIDIARY LEDGER																		
as of		DECEMBER 31, 2023																
		OK	OK	OK	OK	OK	OK	OK	OK	OK	OK	OK	OK	OK	OK	OK	OK	OK
PROJE	IFCA CODE	AX CODE	BUILDING CODE	Package u	REMARKS	DATE RESERV	Contract number	CLIENT'S NAME	TOTAL AREA	TCP	VAT	NTCP	LOAN	PRINCIPAL November 2023	INTEREST November 2023	CLOSING FEE November 2023	PRINCIPAL December 2023	
PMR	PMR-00A-C-0201	PMR-00A-C-02001	Astra	PMR-00A-	Unk	16/08/2017	SC-0000116190	MYLENE CARPOLE MALASAMIC	83.50	5,324,237.20	634,739.70	5,289,437.50	-	5,324,237.08	-	532,424.00	5,324,237.08	
PMR	PMR-00A-C-0202	PMR-00A-C-02002	Astra	PMR-00A-	Unk	11/05/2017	SC-0000110691	SPOUSE DOMINADOR MAXIMO B	28.00	2,388,514.80	-	2,388,514.80	-	2,388,514.80	-	250,794.05	2,388,514.80	
PMR	PMR-00A-C-0203	PMR-00A-C-02003	Astra	PMR-00A-	Unk	16/04/2023	SC-0000185684	PHOENIX ANDREA ORLANDA ALI	28.00	4,825,520.00	517,020.00	4,308,500.00	-	4,825,520.00	-	506,679.60	4,825,520.00	
PMR	PMR-00A-C-0204	PMR-00A-C-02004	Astra	PMR-00A-	Unk	12/02/2017	SC-0000104704	AARON CHRIS LEGASPI UY	28.00	2,235,203.32	-	2,235,203.32	-	840,933.85	266,499.25	101,878.19	847,548.36	
PMR	PMR-00A-C-0205	PMR-00A-C-02005	Astra	PMR-00A-	Unk	10/02/2017	SC-0000103077	JED ALCANTARA SEVILLA	28.00	2,248,192.00	-	2,248,192.00	-	2,248,191.90	-	236,060.16	2,248,191.90	
PMR	PMR-00A-C-0206	PMR-00A-C-02006	Astra	PMR-00A-	Unk	26/10/2017	SC-0000120297	KELVIN JAY GUIAO ROMAS	34.00	2,840,863.20	-	2,840,863.20	-	2,840,863.20	-	289,290.64	2,840,863.20	
PMR	PMR-00A-C-0207	PMR-00A-C-02007	Astra	PMR-00A-	Unk	22/02/2017	SC-0000130084	JAN MICHAEL CANONED LACHIC	32.00	2,565,289.16	-	2,565,289.16	-	2,565,289.16	-	269,355.36	2,565,289.16	
PMR	PMR-00A-C-0208	PMR-00A-C-02008	Astra	PMR-00A-	Unk	12/02/2017	SC-0000104542	KARIZZA JOY DULA ALMONNIA	32.00	2,513,983.38	-	2,513,983.38	-	2,513,983.18	-	263,968.25	2,513,983.18	
PMR	PMR-00A-C-0209	PMR-00A-C-02009	Astra	PMR-00A-	Unk	09/02/2017	SC-0000105588	MA NICOLE DELOS REYES DRIZ	34.00	2,571,555.52	-	2,571,555.52	-	2,571,555.51	-	270,013.33	2,571,555.51	
PMR	PMR-00A-C-0210	PMR-00A-C-02010	Astra	PMR-00A-	Unk	27/10/2017	SC-0000120417	SPOUSES GRACE PAMARAN NA	56.00	4,252,651.20	455,641.20	3,797,010.00	-	4,252,651.20	-	446,528.38	4,252,651.20	
PMR	PMR-00A-C-0211	PMR-00A-C-02011	Astra	PMR-00A-	Unk	17/02/2017	SC-0000104694	LORETO NAVALES SANCHEZ JR.	56.00	4,078,026.47	436,331.41	3,641,695.06	-	4,078,026.47	320,330.21	428,192.78	4,078,026.47	
PMR	PMR-00A-C-0212	PMR-00A-C-02012	Astra	PMR-00A-	Unk	19/02/2017	SC-0000104693	SPOUSES GILMAR ESPEJO CASI	56.00	3,718,864.36	399,449.75	3,320,414.61	-	3,718,864.36	-	390,480.76	3,718,864.36	
PMR	PMR-00A-C-0214	PMR-00A-C-02014	Astra	PMR-00A-	Unk	27/05/2017	SC-0000111542	WALTER BATINGAN YGNACIO	83.50	6,054,361.60	648,681.60	5,405,680.00	-	6,054,361.60	-	635,707.97	6,054,361.60	
PMR	PMR-00A-C-0215	PMR-00A-C-02015	Astra	PMR-00A-	Unk				83.50	-	-	-	-	-	-	-	-	
PMR	PMR-00A-C-0216	PMR-00A-C-02016	Astra	PMR-00A-	Unk				56.00	-	-	-	-	-	-	-	-	
PMR	PMR-00A-C-0217	PMR-00A-C-02017	Astra	PMR-00A-	Unk				56.00	-	-	-	-	-	-	-	-	
PMR	PMR-00A-C-0218	PMR-00A-C-02018	Astra	PMR-00A-	Unk	28/01/2021	SC-0000166639	DANIELLE CALIPES ROYON	34.00	4,685,000.00	501,964.29	4,183,035.71	-	4,685,000.00	-	491,925.00	4,685,000.00	
PMR	PMR-00A-C-0219	PMR-00A-C-02019	Astra	PMR-00A-	Unk	06/04/2022	SC-0000175600	PAULINE GAILE NERY TY	32.00	4,824,540.00	516,915.00	4,307,625.00	-	4,824,540.00	-	506,576.70	4,824,540.00	
PMR	PMR-00A-C-0220	PMR-00A-C-02020	Astra	PMR-00A-	Unk				32.00	-	-	-	-	-	-	-	-	
PMR	PMR-00A-C-0221	PMR-00A-C-02021	Astra	PMR-00A-	Unk	09/02/2017	SC-0000104108	ARVIEE PABLO DE GUZMAN	34.00	2,618,455.27	-	2,618,455.27	-	2,618,455.01	-	274,937.80	2,618,455.01	
PMR	PMR-00A-C-0222	PMR-00A-C-02022	Astra	PMR-00A-	Unk	21/05/2023	SC-0000186816	SPOUSES MANUEL GABAS VIOL	56.00	7,163,800.00	767,550.00	6,396,250.00	-	7,163,800.00	-	283,642.52	7,163,800.00	
PMR	PMR-00A-C-0223	PMR-00A-C-02023	Astra	PMR-00A-	Unk	24/05/2017	SC-0000133000	SPOUSES HELEN GRAY TUCSON	56.00	4,504,276.00	482,601.00	4,021,675.00	-	4,504,276.00	-	472,948.98	4,504,276.00	
PMR	PMR-00A-C-0224	PMR-00A-C-02024	Astra	PMR-00A-	Unk	06/03/2017	SC-0000106001	JOSEF NAN BULICATIN MONJE	56.00	3,967,719.04	425,112.75	3,542,606.29	-	3,967,719.03	-	416,610.50	3,967,719.03	
PMR	PMR-00A-C-0225	PMR-00A-C-02025	Astra	PMR-00A-	Unk				83.50	-	-	-	-	-	-	-	-	
PMR	PMR-00A-C-0301	PMR-00A-C-03001	Astra	PMR-00A-	Unk	24/08/2018	SC-0000138474	THEA JANE GERMINO GEMORAJ	83.50	6,676,044.40	715,290.47	5,960,753.93	-	6,676,044.40	-	700,984.66	6,676,044.40	
PMR	PMR-00A-C-0302	PMR-00A-C-03002	Astra	PMR-00A-	Unk	28/05/2017	SC-0000111601	SPOUSES MYLENE DEGUMA DEL	28.00	2,284,791.60	-	2,284,791.60	-	2,284,791.61	-	239,903.12	2,284,791.61	
PMR	PMR-00A-C-0303	PMR-00A-C-03003	Astra	PMR-00A-	Unk	27/05/2017	SC-0000111649	FRANCES MEYER BARLES VILLA	28.00	2,305,320.40	-	2,305,320.40	-	2,305,320.40	-	242,121.64	2,305,320.40	
PMR	PMR-00A-C-0304	PMR-00A-C-03004	Astra	PMR-00A-	Unk	09/02/2017	SC-0000104272	GERAVIL ECUBE ELLIMAE LEE E	28.00	2,151,278.90	-	2,151,278.90	-	2,151,278.90	-	225,884.28	2,151,278.90	
PMR	PMR-00A-C-0305	PMR-00A-C-03005	Astra	PMR-00A-	Unk	12/02/2017	SC-0000105453	JEAN ROSE SOLIDARIOS DEGAB	28.00	2,195,182.56	-	2,195,182.56	-	2,195,182.56	457,864.34	230,494.17	2,195,182.56	
PMR	PMR-00A-C-0306	PMR-00A-C-03006	Astra	PMR-00A-	Unk	10/02/2017	SC-0000103110	SPOUSES VIRGLIO DOMINGO W	34.00	2,464,087.52	-	2,464,087.52	-	2,464,087.52	-	259,723.19	2,464,087.52	


Solutions

Context Diagram

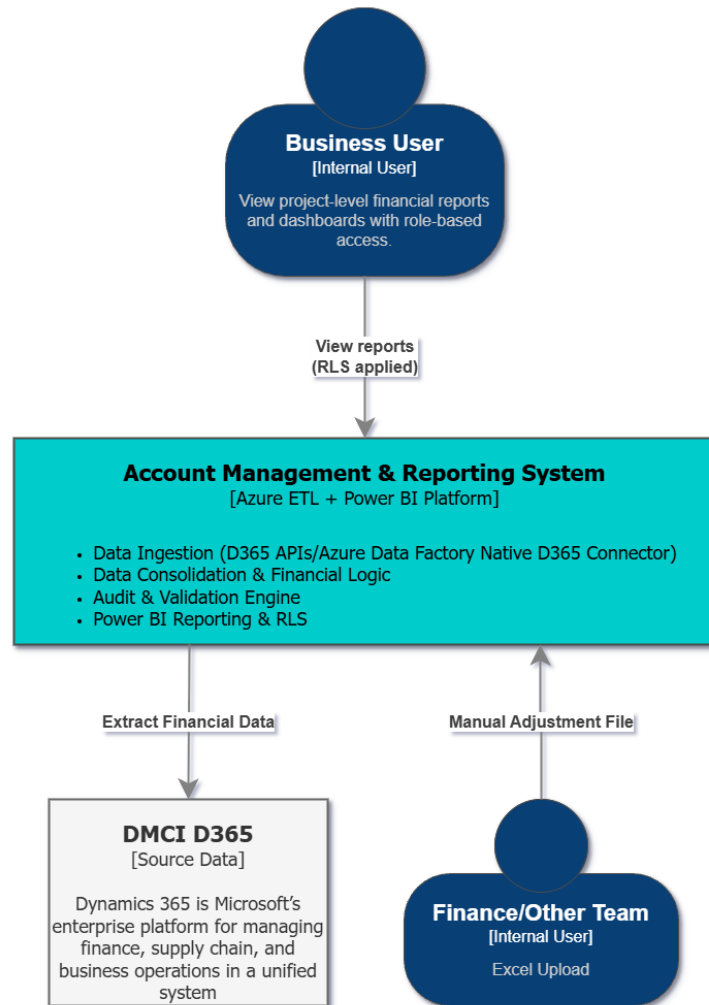


- Automates financial data extraction from D365 via secure APIs/Azure Data Factory Native D365 Connector
- Consolidates system data and manual adjustments into a centralized platform
- Executes financial logic, validation, and audit checks in Azure
- Delivers secure Power BI dashboards with role-based access (RLS)
- Eliminates manual Excel processing and improves reporting efficiency

High Level Solution

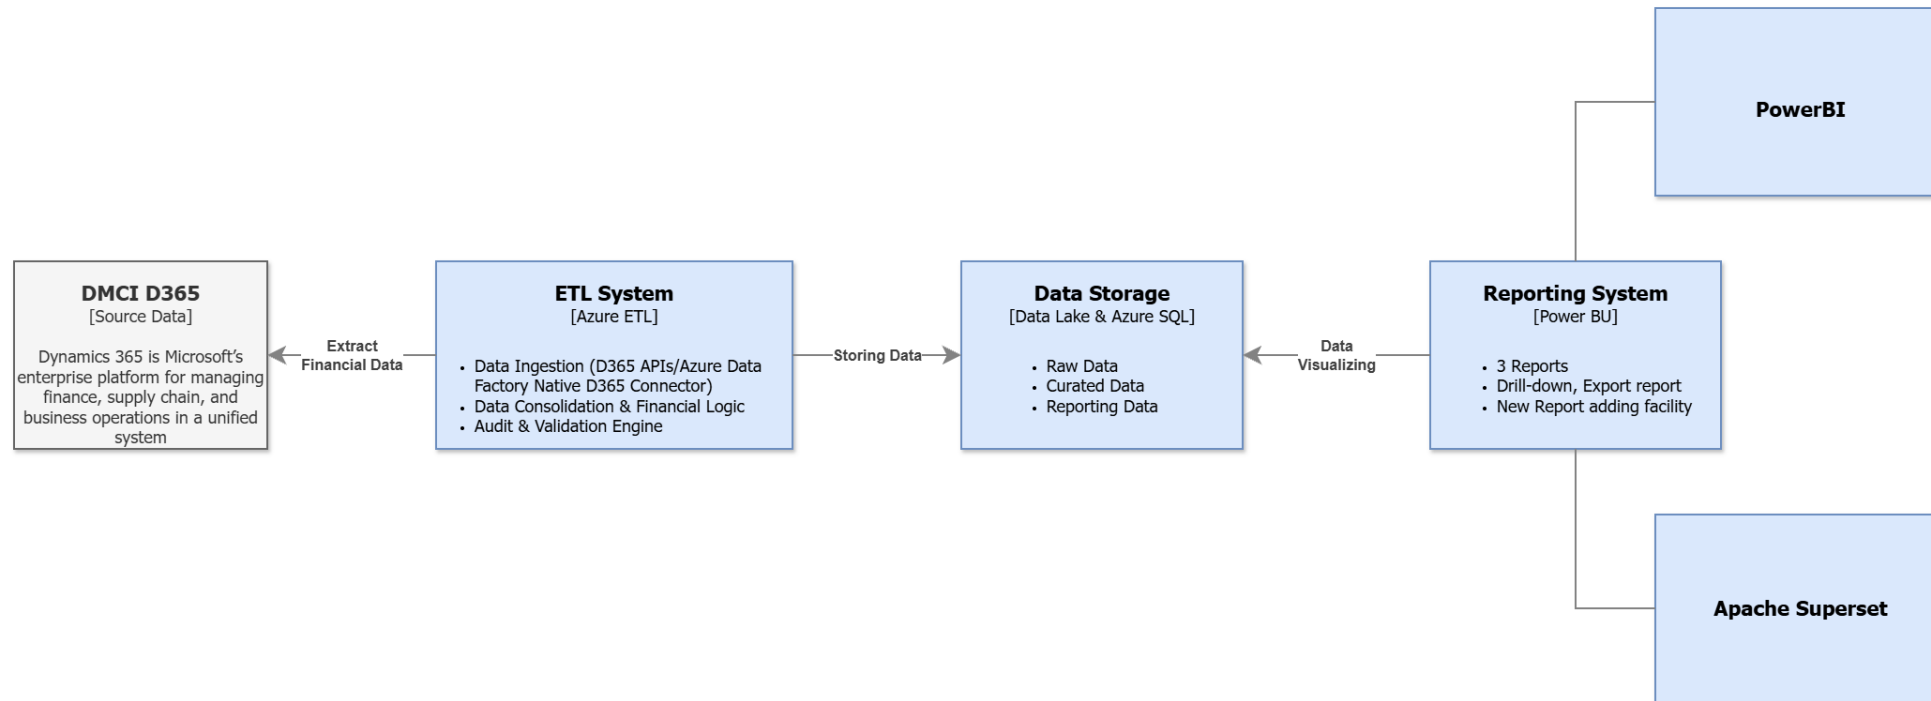


- Extracts financial data from D365 through an automated Azure ETL process
- Consolidates and validates data with embedded financial logic
- Stores raw, curated, and reporting data in Data Lake & Azure SQL
- Delivers interactive reports via Power BI or Apache Superset
- Enables drill-down, export, and scalable report creation

Solution Architecture

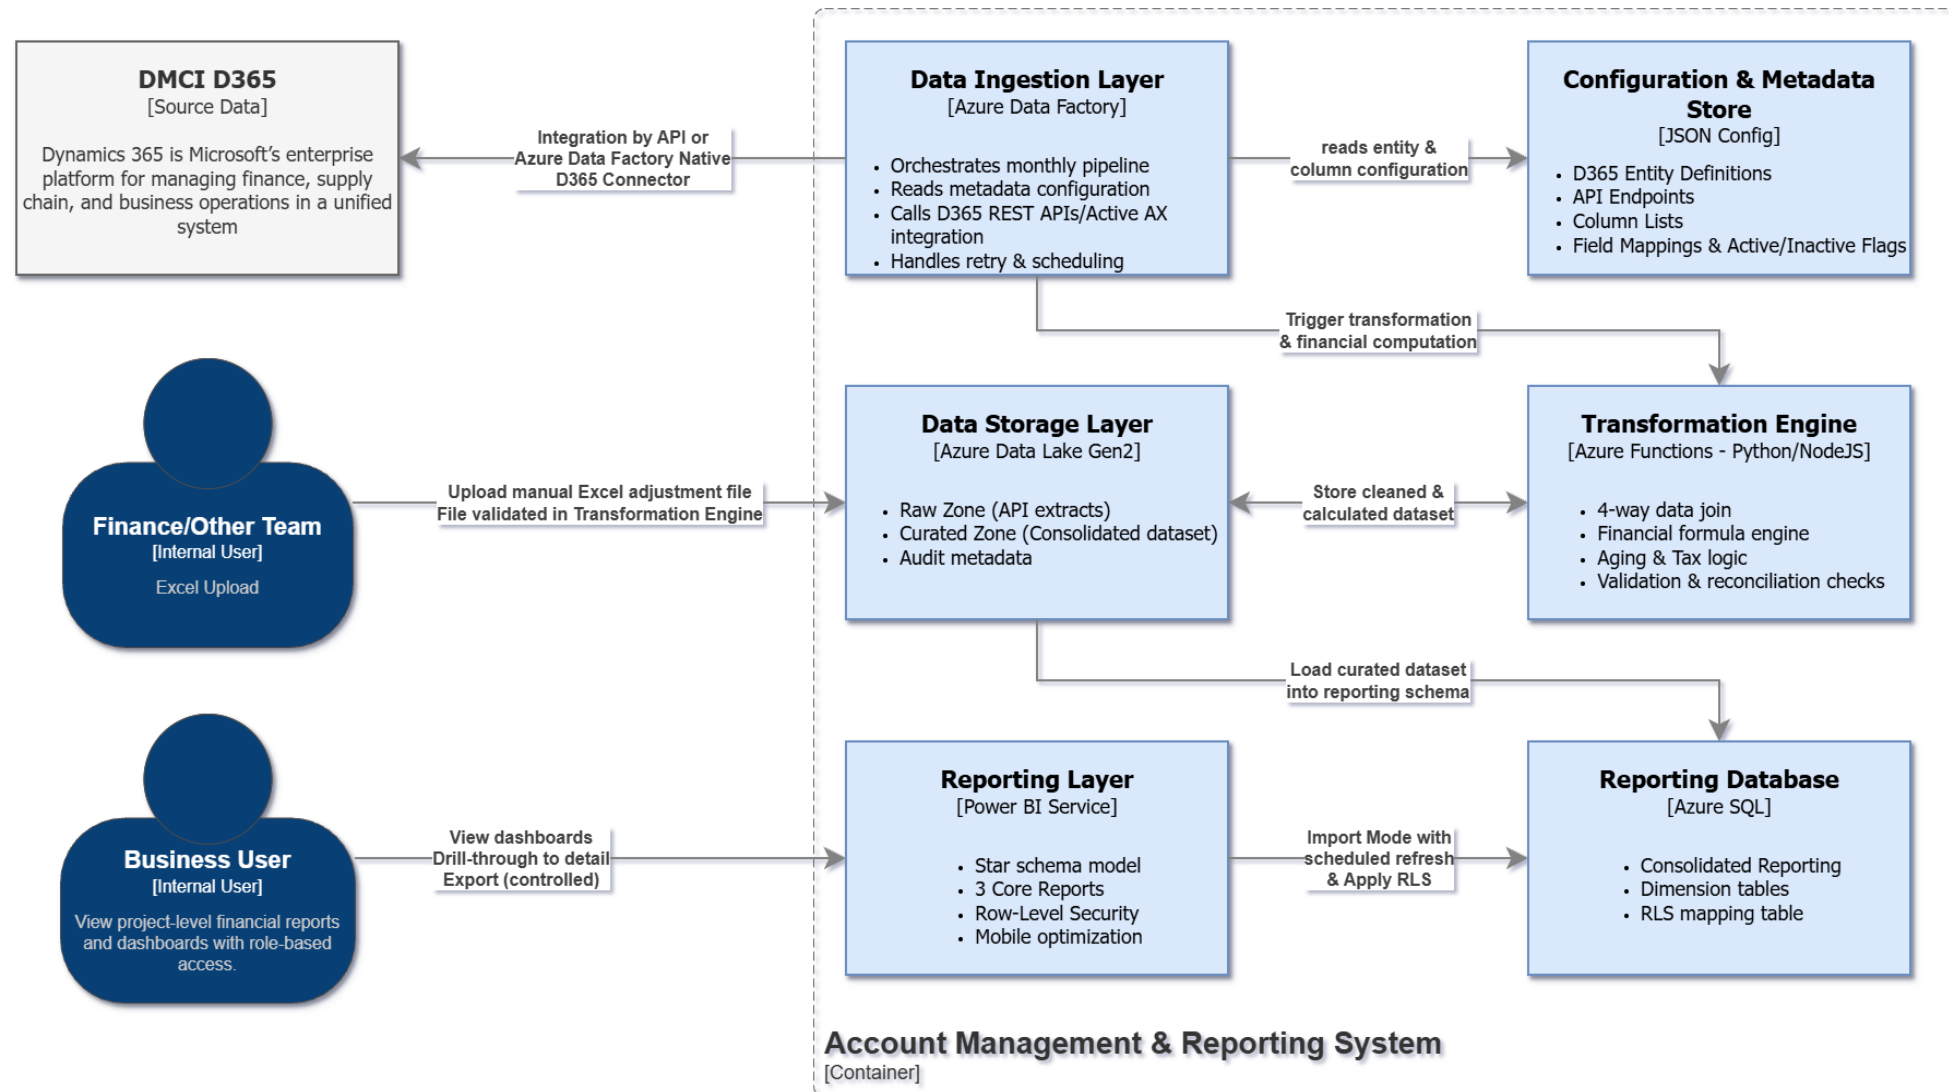

Manual File Upload Flow

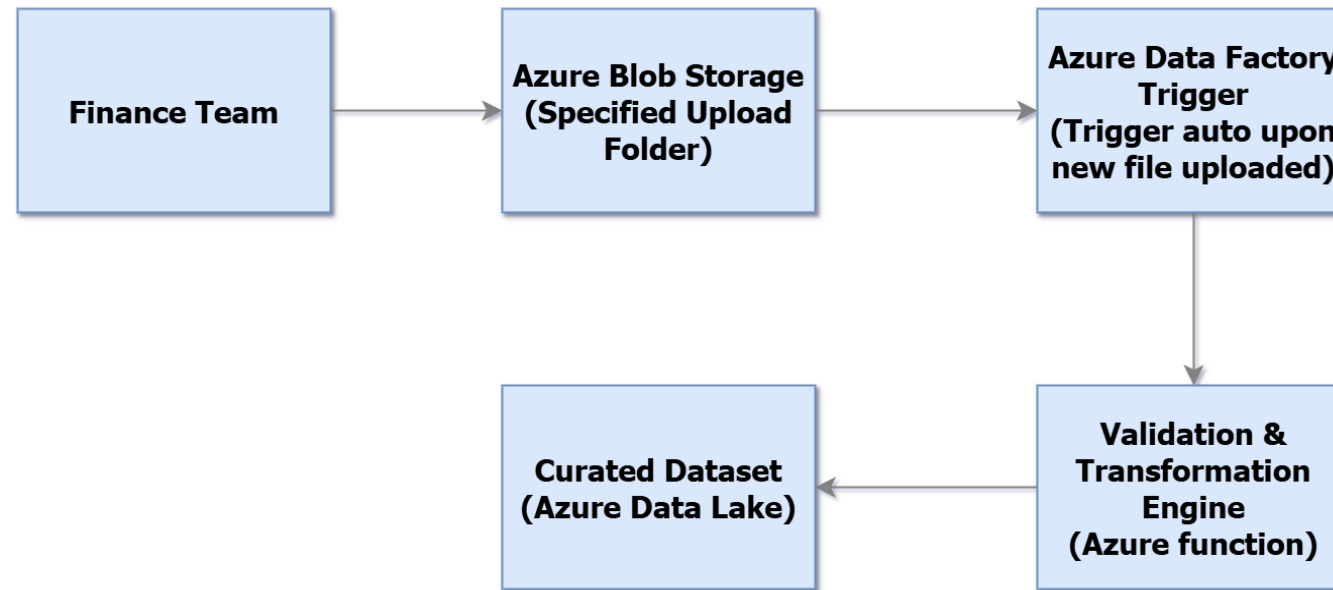

- Finance Team uploads the monthly adjustment file to Azure Blob Storage
- Azure Data Factory trigger detects the new file automatically
- Validation & Transformation Engine processes and verifies the data
- Approved data is loaded into the curated dataset for reporting

Why Reporting Engine (Power BI / Superset)?

- **Easy to Use & Interactive** – Users can filter, search, and drill into data instantly without relying on IT
- **Secure Access Control** – Each user automatically sees only the projects or data they are authorized to view
- **Generate New Reports Easily** – Users can create new reports or views from the same dataset without rebuilding Excel files
- **Faster & Automated Updates** – Reports refresh automatically, eliminating manual consolidation work
- **Accurate & Consistent Information** – Everyone works from the same validated data, reducing errors and confusion

Power BI vs Apache Superset vs Custom Web

Evaluation Criteria	Power BI	Apache Superset	Custom Web Application
License Cost	~\$14/user/month (Pro)	Free (open source)	No License Cost
Infrastructure Cost	-	Must host & maintain	Must host & maintain
Setup Complexity	Very low	Medium-High	Medium-High
Initial User Size (20-25 users)	Excellent fit	Acceptable	Over-engineered
Ease of Use (Finance Users)	Very user-friendly	More technical	Depends on custom UI
Row-Level Security (RLS)	Built-in & simple	Requires setup	Requires full custom build
Financial Governance	Strong	Moderate	Depends on implementation
Infrastructure Management	Microsoft-SaaS managed	Self-managed	Self-managed
Development Effort	Low	Medium	Very High
Scalability (50-100 users)	Good	Good	Depends on design
Cost Predictability	License-based	Infra-based	Development-heavy
Maintenance Overhead	Very Low	Medium-High	Low-High (custom)
Time to Implement	Fast	Medium	Slow

3-Year Cost Comparison (25 Users)

Reporting Engine Cost Only (Excluding Azure Infrastructure Costs for ETL)

Cost Category	Power BI (25 Users)	Apache Superset/Custom Web
Monthly Cost	~\$350	~\$900
Annual Cost	~\$4,200	~\$10,800
3-Year Total	~\$12,600	~\$32,400

<Recommended Approach>

- If the priority is ease of use, strong governance, built-in security, enterprise integration, and minimal infrastructure management, Power BI
- If the primary priority is supporting a very large user base with minimal per-user licensing cost, Apache Superset can be considered.
- If the requirement extends beyond reporting into custom workflows, approvals, or transactional system functionality, a custom web application may be justified, though it involves higher development and operational overhead.

Why a Separate Admin Web Application Is Not Considered



- In this phase, a separate Admin Web Application is not considered
- Configuration is managed within the ETL layer to ensure faster implementation
- The priority is to establish the reporting system quickly and efficiently
- Adding an admin layer now would increase development effort and Azure cost
- An Admin Web Application can be considered in a later phase if business needs evolve

Scope of Work



Scope

- ☐ Requirement Analysis and Planning
- ☐ ETL Process Development
- ☐ Power BI Development
- ☐ Testing and Quality Assurance (Chrome and Edge browsers for Windows, and on Chrome and Safari for macOS)
- ☐ Azure Server Configuration (Development, Stage and Production)
- ☐ Design Documents:
 - ☐ User manual for Power BI
 - ☐ Deployment manual for ETL Process
 - ☐ Architecture diagrams
- ☐ Security implementation & validation
- ☐ Training, UAT Support & Bug fixing

Out of Scope

- ☐ Development of a separate Admin Web Application
- ☐ Custom workflow or approval portal development
- ☐ Third-party system integrations beyond defined D365
- ☐ Advanced penetration testing or external security audits
- ☐ Data Migration

Task Details (ETL Process & Power BI)

ETL Tasks Details (1/2)

#	Main Task	Subtask	Description
1	Discovery & Architecture Planning	Requirement Analysis	Gather business, data, SLA & security requirements
		Source System Analysis and Linked Services Configuration	Analyze D365 AX & other data sources
		Environment Strategy Definition	Define DEV / STAGE / PROD separation
		Data Flow Design	End-to-end ETL & orchestration
2	Azure Subscription & Governance	Subscription Validation	Validate existing or create Azure subscription
		Resource Group Structure	Design RG structure per environment & workload
		Tagging Strategy	Define cost, owner, environment tags
		RBAC Design and Implementation	Design RBAC roles for DevOps, Ops, Read-only
3	Azure Data Factory	Data Extraction Pipelines	Extract data from D365 AX & others
		Data Transformation Logic	Mapping, cleansing, enrichment
		Triggers & Scheduling	Time / event-based triggers
		Parameterization & Config	Environment-based configuration
4	Azure Storage Account	Storage Account Provisioning	Create ADLS Gen2 / Blob storage
		Container / File System Design	Raw / Curated / Processed zones
		Folder Structure Definition	Data domain & source-based layout
		Security & Access Configuration	RBAC, managed identity access
		Network Security	Private endpoint / firewall rules
		Encryption & Data Protection	Encryption, secure transfer

ETL Tasks Details (2/2)

#	Main Task	Subtask	Description
5	Azure Functions	Function App Provisioning	Create Function App (Consumption/Premium)
		Runtime & Configuration	Configure runtime, app settings
		ADF Integration and Security Configuration	Invoke Functions from ADF pipelines
6	Azure DevOps	Project & Repo Setup	Create Azure DevOps project & repos
		Branching Strategy	Define Git branching model
		Variable Groups & Secrets	Key Vault integration
		ADF CI/CD Integration	Publish & promote ADF pipelines
7	Monitoring, Alerting & Operations	ADF Monitoring Setup	Pipeline runs, failures, retries
		Azure Function Monitoring	Function logs & metrics
		Alert Rules Configuration	Failure, latency, threshold alerts
		Email Notification Setup	Action groups & email alerts

Power BI Reports




#	Reports	Summary
1	BSL Details Report	• RBAC- Role Based Authentication • Power BI BSL Details Report • Dashboard & Graph • Example Excel File name: 12. Consolidated BSL, Tax Sorting, CAL and Costing as of December 31, 2026
2	BSL Summary Report	• RBAC- Role Based Authentication • Power BI BSL Summary Report • Dashboard & Graph • Example Excel File name: 12. Consolidated BSL, Tax Sorting, CAL and Costing as of December 31, 2026
3	Tax Sorting Report	• RBAC- Role Based Authentication • Power BI Tax Sorting Report • Dashboard & Graph • Example Excel File name: 12. Consolidated BSL, Tax Sorting, CAL and Costing as of December 31, 2026

Power BI Tasks Details

#	Tasks	Task Summary
1	Data Preparation	- Identify and connect to data sources (database, data lake, APIs, files) - Clean data (remove duplicates, handle nulls, correct formats) - Transform data using Power Query (filtering, merging, splitting) - Standardize naming conventions and data types - Create calculated columns where required
2	Data Modeling	- Design fact and dimension tables (star / snowflake schema) - Define relationships between tables - Create DAX measures (KPIs, aggregations, ratios) - Optimize model performance (cardinality, data types) - Implement row-level security (RLS) if required
3	Report Design	- Identify business requirements and key metrics - Design report layout and page structure - Define report navigation (pages, drill-through) - Apply consistent themes, colors, and branding - Prepare wireframes or mockups for approval
4	Visualization Development	- Build charts, tables, and KPI visuals - Implement slicers and filters for interactivity - Enable drill-down and drill-through functionality - Apply conditional formatting - Ensure visuals follow best practices and readability
5	Testing and Validation	- Validate data accuracy against source systems - Test calculations, measures, and filters - Verify performance and load times - Check security rules and user access - Fix defects and inconsistencies
6	Deployment and Training	- Publish reports to Power BI Service - Configure datasets, gateways, and refresh schedules - Set workspace roles and permissions - Share reports and dashboards with users - Conduct end-user training and provide documentation

Azure ETL Diagram & Costing

DMCI ETL Diagram

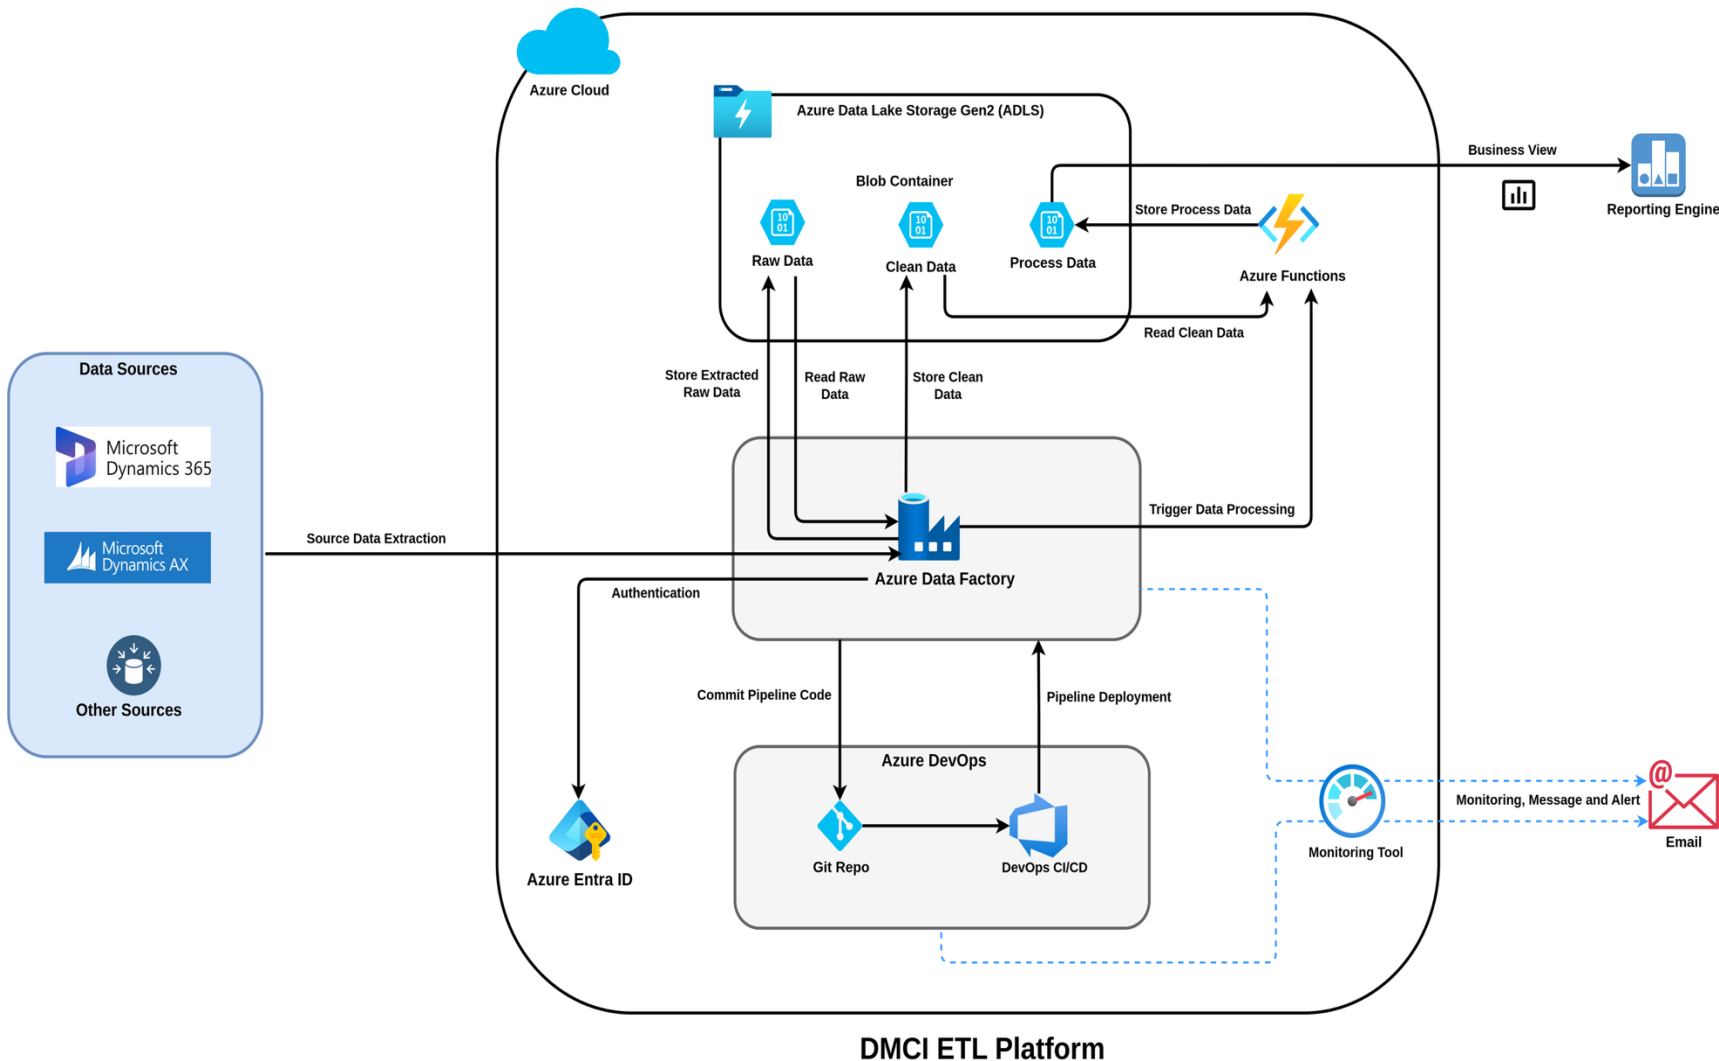

- Data is sourced from Microsoft Dynamics 365, Dynamics AX, and other systems
- Azure Data Factory performs secure data extraction and orchestration
- Extracted data is stored in Azure Data Lake Storage Gen2
- Data is organized into Raw, Clean, and Processed layers
- Azure Functions execute data transformation and processing logic
- Processed data is prepared for business reporting and analytics
- Reporting engine provides business insights and dashboards
- Azure DevOps manages source control and CI/CD for ETL pipelines
- System monitoring, alerts, and notifications are enabled via email
- Azure Entra ID ensures authentication and access security

DMCI ETL Platform Details



#	Items	Summary
1	Data Sources	• Microsoft Dynamics 365 • monthly adjustment excel file
2	Data Ingestion	• Azure Data Factory (ADF) extracts data from source systems • Secure authentication handled via Azure Entra ID
3	Data Storage (Azure Data Lake Storage Gen2 – ADLS)	• Raw Data Zone: Stores extracted raw data • Clean Data Zone: Stores validated and transformed data • Process Data Zone: Stores aggregated/processed data for reporting
4	Data Processing	• Azure Data Factory reads raw data and writes clean data • Azure Functions are triggered for data transformation and processing • Processed data is stored back into ADLS
5	Business & Reporting Layer	• Reporting Engine consumes processed data • Provides Business View/Power BI for analytics and reporting
6	DevOps & CI/CD	• Pipeline code maintained in Git Repository • Azure DevOps CI/CD used for pipeline deployment • Continuous integration and deployment of ADF pipelines
7	Monitoring & Alerts	• Central monitoring tool tracks pipeline execution • Automated alerts and notifications sent via Email
8	Cloud Platform	• Entire solution runs on Azure Cloud • Designed for scalability, security, and automation


Azure Server Cost "DMCI ETL" (Stage/Production)



Service category	Service type	Region	Description	Estimated monthly cost
Analytics	Azure Data Factory	Southeast Asia	Azure Data Factory V2 Type, Data Pipeline Service Type, Azure Integration Runtime: 60 Activity Run(s), 100 Data movement unit(s), 1,000 Pipeline activities, 0 Pipeline activities – External,	\$90.00
Developer tools	Azure DevOps		0 Basic Plan license additional users, 0 Basic + Test Plans license users, Paid tier - 1 Microsoft Hosted Pipeline(s), 1 Self Hosted Pipeline(s), 0 GB Artifacts, GitHub Advanced security - 0 committers covered by code security and 0 committers covered by secrets protection	\$40.00
Compute	Azure Functions		Flex Consumption tier, 4096 MB Instance memory size, 1,000 x10 On demand executions per month, 1,000 Active on demand executions seconds per instance, 100 Active on demand instances	\$11.10
Storage	Storage Accounts		Premium Block Blob Storage, Hierarchical Namespace, LRS Redundancy, Hot Access Tier, 100 GB Capacity - Pay as you go, 10 x 10,000 Write operations, 10 x 10,000 Read operations, 10 x 10,000 Iterative Read operations, 10 x 100 Iterative Write operations, 1,000 GB Data Retrieval, 1,000 GB Data Write, SFTP disabled, 1,000 GB Index, 1 x 10,000 Other operations	\$20.67
		Total		\$161.77

Power BI Costing

Power BI Costing

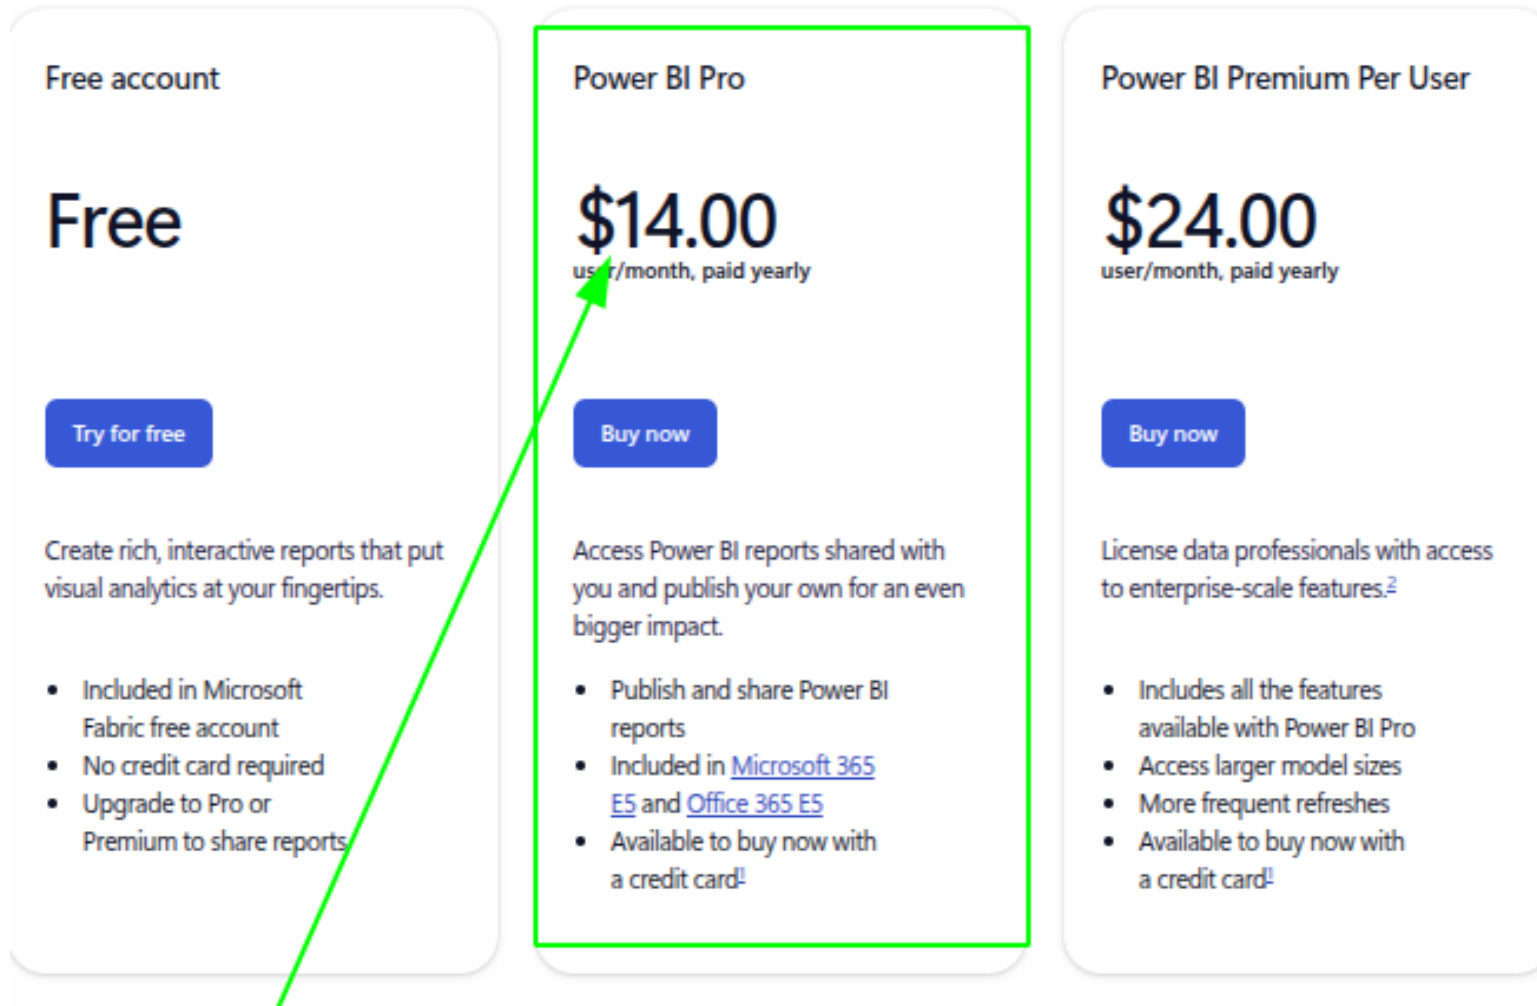

Free account	Power BI Pro	Power BI Premium Per User
Free	\$14.00 user/month, paid yearly	\$24.00 user/month, paid yearly
Try for free	Buy now	Buy now
Create rich, interactive reports that put visual analytics at your fingertips.	Access Power BI reports shared with you and publish your own for an even bigger impact.	License data professionals with access to enterprise-scale features. ²
• Included in Microsoft Fabric free account • No credit card required • Upgrade to Pro or Premium to share reports	• Publish and share Power BI reports • Included in Microsoft 365 E5 and Office 365 E5 • Available to buy now with a credit card¹	• Includes all the features available with Power BI Pro • Access larger model sizes • More frequent refreshes • Available to buy now with a credit card¹

Note: BJIT has considered the **Power BI Pro Package**


Resource Allocation & Cost

Project Total Effort & Cost Quotation

#	Resource	Rank	Unit price In USD (Monthly)	M1	M2	M3	Total Efforts (man-month) & Cost in USD
1	Project Manager	6		0.25	0.25	0.25	0.75
2	Sr. Software Engineer (Azure Functions)	5		1.00	1.00	1.00	3.00
3	Sr. Software Engineer (PowerBI)	5		1.00	1.00	1.00	3.00
4	Sr. SQA	5		0.50	0.50	0.50	1.50
5	Sr. DevOps Engineer	5		1.00	1.00	1.00	3.00
Total Effort and Cost in USD				3.75	3.75	3.75	11.25

Team Execution,
Roles and Responsibilities,
Pre-requisites,
Payment Terms & Conditions

Project Organizational Chart

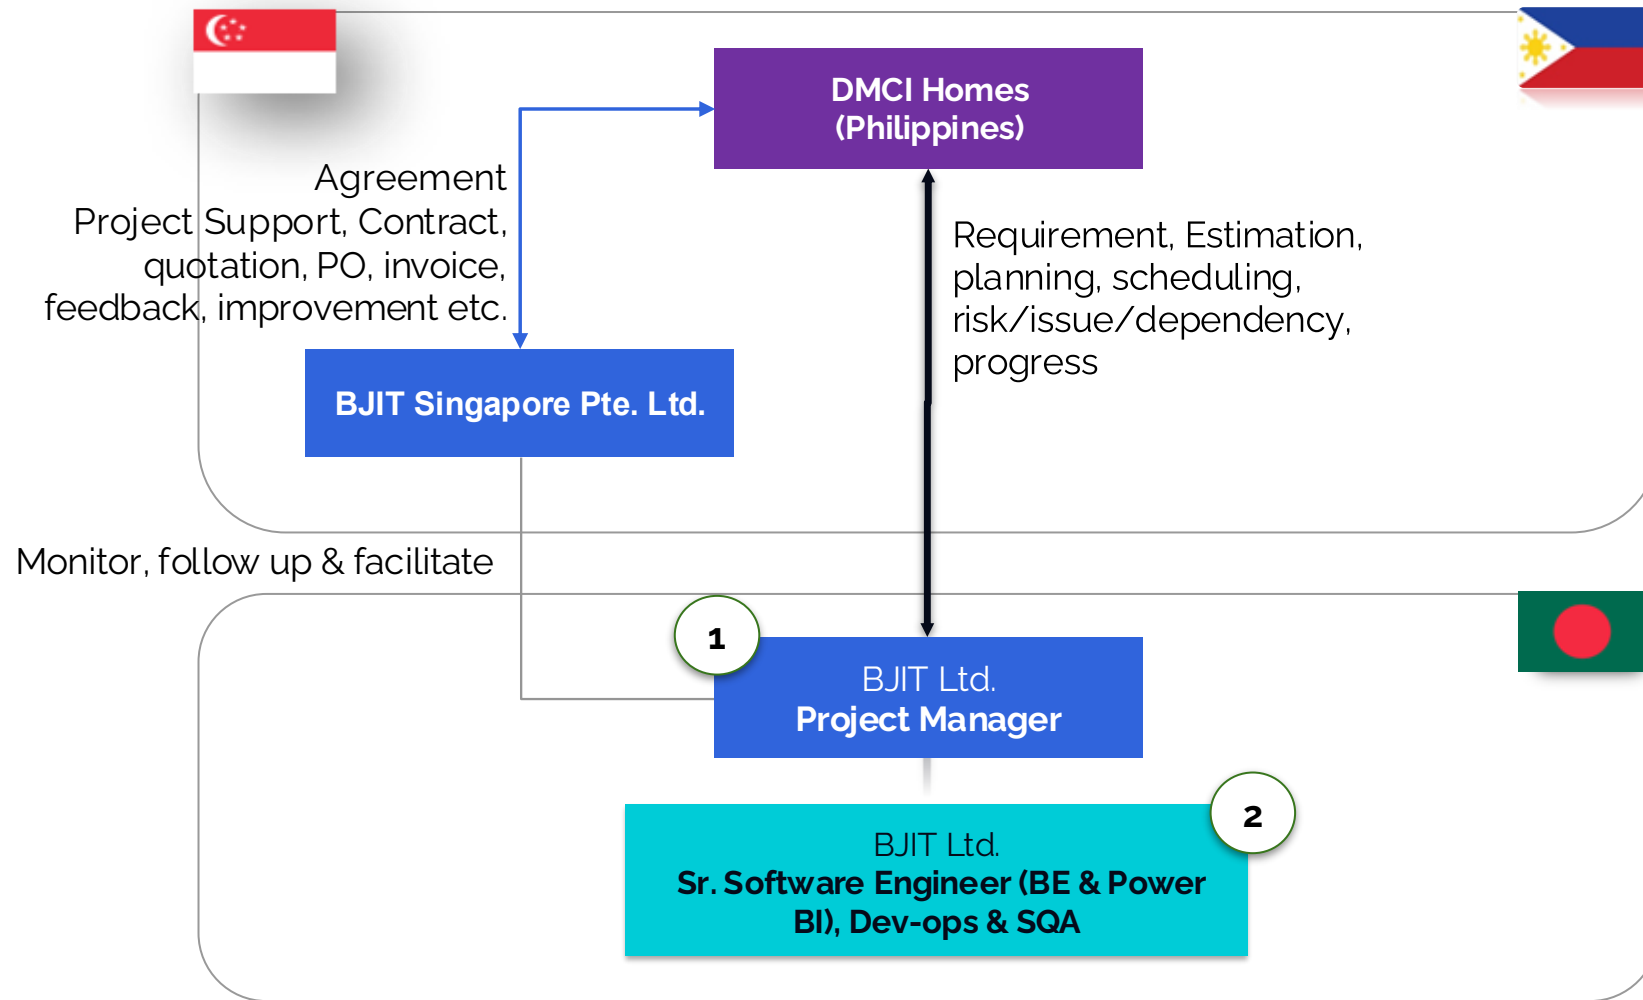

The number of staff can be added or removed based on the volume of work

Project Role and Responsibilities

#	Role	Responsibilities
1	Project Manager	1. Ensure all functional and non-functional requirements are aligned with stakeholders 2. Define key phases (development & testing) and monitor progress against deadlines 3. Facilitate collaboration between developers, and testers to ensure smooth execution 4. Prepare and update project progress in PM tools 5. Review the source code & design documents 6. Assign tasks to offshore team members and follow up
2	Software Engineer (Power BI & Back-End)	1. Design and build optimized data models for analytics 2. Develop interactive Power BI reports and dashboards 3. Extract, transform, and load data from multiple sources 4. Automate and monitor ETL pipelines for reliable data refresh
4	SQA	1. Design, implement, and execute test plans for frontend and backend. 2. Develop and maintain automated testing frameworks. 3. Identify, report, and track software defects and performance issues. 4. Ensure software meets security and compliance standards. 5. Collaborate with developers to improve code quality and stability.
5	DevOps Engineer	1. Azure ETL cloud configurations for dev, staging and production environment 2. Preparing cost estimation and Azure architecture diagram 3. Preparing Deployment manual, Support application deployment

Agile Delivery & Sprint-Based Estimation Approach



Agile Delivery Model

- The engagement is executed as a time-boxed agile engagement of approximately **3 months**
- Requirements are managed through a Product Backlog, owned and prioritized by the DMCI Product Owner
- No fixed feature scope is committed upfront for the entire duration

Sprint-Based Estimation & Commitment


- The project is delivered in short, **iterative sprints (2 weeks)**
- At the start of each sprint, BJIT provides:
 - Detailed effort estimation (Story points/estimated hour based on the assigned resources)
 - Feasibility assessment
 - Delivery risks (if any)
- Only the scope selected for the current sprint is committed

Sprint Execution & Review

- During each sprint:
 - Features are designed, implemented, and tested
 - Documentation is updated as “living documentation”
- At the end of each sprint:
 - Delivered items are reviewed with DMCI
 - Completion status and quality are confirmed
 - Remaining backlog is re-evaluated


Continuous Re-Planning

- Based on sprint outcomes:
 - Backlog priorities may be adjusted
 - Scope for subsequent sprints is re-estimated
- This ensures:
 - Maximum value delivery within the timebox
 - Transparency of progress and remaining effort

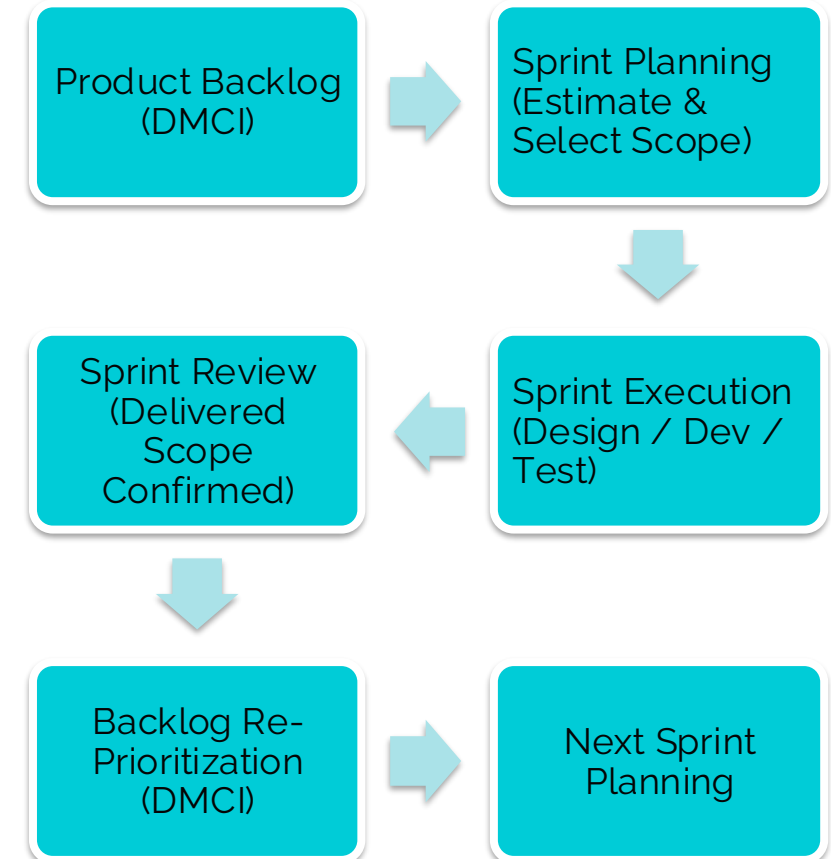

Note: Delivery will be managed through a sprint-based Agile approach over the 3-month period. Scope commitment and feature completion will be determined iteratively per sprint, based on agreed priorities, progress, and available capacity.

High Level Schedule (Phase1 MVP)

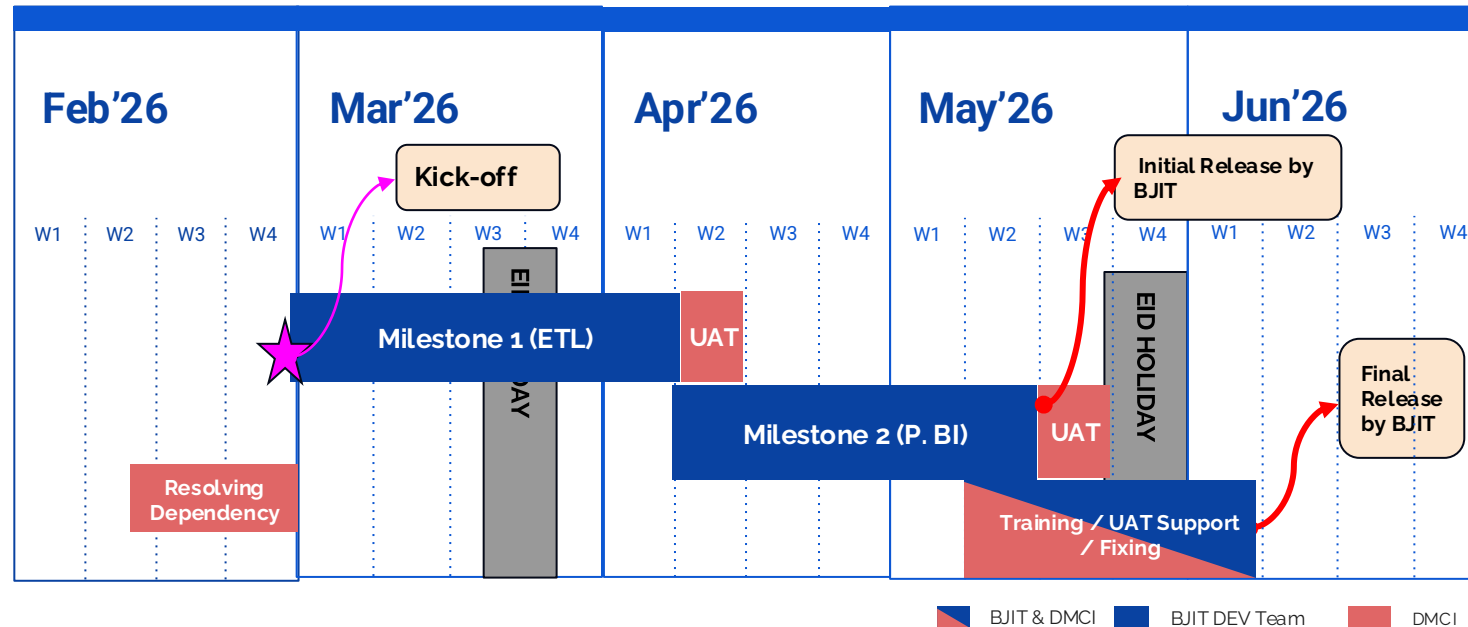

Notes:

- This project will be executed using a time-boxed Agile delivery model, where sprint scope is defined through backlog prioritization and sprint planning, rather than being fixed upfront for the entire project duration
- Delivery will be aligned with agreed sprint priorities and available team capacity, ensuring continuous value delivery and flexibility to adapt to evolving business needs
- Any adjustments related to schedule, scope, or resource allocation will be jointly discussed and mutually agreed upon by DMCI and BJIT
- Features will be delivered incrementally based on sprint outcomes achieved within the contract period

Pre-Requisites (1/2) - Reporting & Business Inputs



- 3 Reports description of purpose, target users, and expected outputs
- Formal written documentation of financial formulas and business logic
 - Collection calculations
 - Outstanding balance logic
 - Revenue recognition (POC) rules
 - Tax computation logic etc
- Documented explanation of report columns
 - Column definitions
 - Data source reference (D365 entity/field or manual input)
 - Calculation dependency (if derived field)
- Formal specification of manual adjustment file format
 - Required columns
 - Data types
 - Validation rules
 - Upload frequency
 - Approval process (if applicable)
- Agreement on reconciliation tolerance, defined as $\pm 0.01\%$ variance against validated Excel outputs
- DMCI shall provision at least one active **Power BI Pro license** to enable report development, workspace configuration, publishing, and validation activities during the implementation phase.

Pre-Requisites (2/2) – ETL & Azure



#	Category	Details
1	System Confirmation	• Confirmation whether any historical BSL data remains in Dynamics AX • If AX data exists: ◦ Scope of data required (years/entities) ◦ Access method for extraction (DB export / file export)
2	D365 Data Access	• Access to required D365 environments (Sandbox + Production) • API access enabled for: ◦ All Property Units ◦ CWT Data ◦ BSL Data • OAuth2 authentication setup • Required API permissions granted
3	Azure Environment Readiness	• Azure subscription (Dev, Stage, Prod environments) • Resource group creation approval • Access to configure: ◦ Azure Data Factory ◦ Azure Functions ◦ Azure Data Lake Gen2 ◦ Azure SQL Database • Key Vault access • Network/security approval

Payment Terms and Conditions

Contract Type & Payment

- This agreement will follow the BJIT **Labo Base Contract (Labo)** model
- Contract costs will be paid on time as per BJIT Labo policy
- **Project billing will be on a monthly basis**
- Payments must be made within **30 days** from the date BJIT issues the invoice
- A valid **Project Contract Purchase Order (PO)** must be issued before project commencement

Transport & Relocation Costs

- Customers are responsible for any specific transport costs of devices required for project development or management when relocation is involved

Holidays & Leave Policy

- BJIT follows the Bangladesh Government Holiday Calendar
- Engineers will be off on declared holidays
- BJIT will share the yearly holiday calendar in advance
- If engineers are required to work on a holiday, the customer must notify BJIT beforehand
- For any engineer's personal leave, BJIT will inform the customer in advance and obtain approval

Working Hours

- Standard operating hours are 8:30 AM – 5:30 PM BST (Bangladesh Standard Time), Monday to Friday
- Working hours may be adjusted based on necessity, urgency, or project importance, upon mutual agreement

Additional Tools & Licenses

- Costs for any additional testing devices, software licenses, cloud licenses, or other required tools will be borne by the DMC I

Communication Method, Development Approach, Methodology, Process & Deliverables

Proposed Communication Method

#	Category	Contents	Language	Remarks	Notes
1	Mail	BJIT Email/DMCI Email	English	BJIT/DMCI	
2	Chat/Meeting	Teams	English	BJIT	BJIT proposes using its own communication tools like On Going Projects with DMCI
3	File Sharing	Sharepoint	English	BJIT	
4	Project Management	Jira	English	BJIT	

Meeting Calendar

Meeting type	Frequency	Topics	Owner	Attendee	Meeting format
Kick-off meeting	Once: 1 hour	- Team introduction, different processes/meeting/reporting/tool finalization	DMCI	(DMCI) Management (BJIT) All team members, sales & ED support team	Remote in Teams
Scrum	Daily: 30 min	- Yesterday's update, today's plan, any blocker/risk/issue/dependency	BJIT	(DMCI) Product Owner (Optional) (BJIT) All team members, section head (optional)	Remote in Teams
Sprint planning meeting	Bi-weekly: 1 hour	- Finalizing scope of the sprint	BJIT	(DMCI) Product Owner (BJIT) All team members, section head(optional)	Remote in Teams
Progress Conference/Status update	Weekly: 1 hour	- Progress status update, burn down status, risk/issue/dependency	BJIT	(DMCI) Product Owner (BJIT) All team members, section head	Remote in Teams
Review/Sprint demo & retro	Bi-weekly: 1 hour	- Sprint delivery demo, what went well, what went wrong, improvement action points	BJIT	(DMCI) Management, Product Owner (BJIT) All team members, section head	Remote in Teams
Q&A clarification meeting	On demand	- Q&A clarification	BJIT	(DMCI) Product Owner (BJIT) All team members, section head (optional)	Remote in Teams
Feedback sharing meeting	Monthly: 1 hour	- Team performance status, contract related discussion, scale up/down, future plan	DMCI	(DMCI) Management, (BJIT) BSE, Sales & ED MGT team	Remote in Teams

Development Environment & Required Items

#	Category	Contents	Provider	Remarks
1	Work Location	Offshore: Dhaka	BJIT	
2	Device	Work device: Laptop	BJIT	
3	Deployment Technology	Microsoft Dynamics 365 & AX, ADF, Blob, Power BI, Node JS/Python	BJIT	
4	Cloud	Azure	DMCI	<i>DMCI will provide Azure server</i>
5	Management Tool	Source Code Management: Gerrit	BJIT	<i>BJIT proposes using its own communication tools like On Going Projects with DMCI</i>
		Task Management and Test Management: Jira	BJIT	
		Document Management: Sharepoint	BJIT	

Implementation Approach



UI/UX & System Design



Development & Testing



Cloud Service Procurement



Infrastructure Setup



Release



Training



Support & Maintenance



Handover

Development Methodology

Key Benefits

- ❑ **Iterative Development:** Work is delivered in small, usable increments (called sprints), **BJIT follows 2 weeks sprint**
- ❑ **Customer Collaboration:** Continuous feedback from users and stakeholders shapes the product
- ❑ **Responding to Change:** Agile embraces evolving requirements—even late in the process
- ❑ **Cross-functional Teams:** Designers, developers, and testers work together throughout



Agile

Why Agile?

- ❑ Faster time to product release
- ❑ Better product quality through continuous testing
- ❑ Greater visibility and control over progress
- ❑ Reduces risk by delivering value early and often

Note: Scope commitment is determined sprint by sprint based on priority and capacity

Sprint Activity

SI	Activity	BJIT	DMCI
1	Backlog updating	C	R/A
2	Backlog grooming	R/A	C
3	Sprint planning	R	A/C
4	Sprint development & Bug fixing	R/A	I
5	Design review	R	A/C
6	QA test case writing	R	I
7	Internal Release 1	R/A	I
8	QA Testing	R	I
9	Internal Release 2	R/A	I
10	QA Report	R	I
11	Sprint Release (deliverables)	R	A
12	Sprint Demo	R	A
13	Sprint Retrospective	R	C
14	UAT	C	A/R

R = Responsible (does the work)

A = Accountable (owns the outcome)


C = Consulted (provides input)

I = Informed (kept in the loop)

Note: Sprint scope is finalized per sprint under an agile model. The Product Backlog is owned by DMCI, and delivery is based on sprint outcomes.

Proposed Agile Development Process

Scope and delivery will be managed through Agile sprint planning, enabling flexible prioritization and incremental value delivery throughout the project.

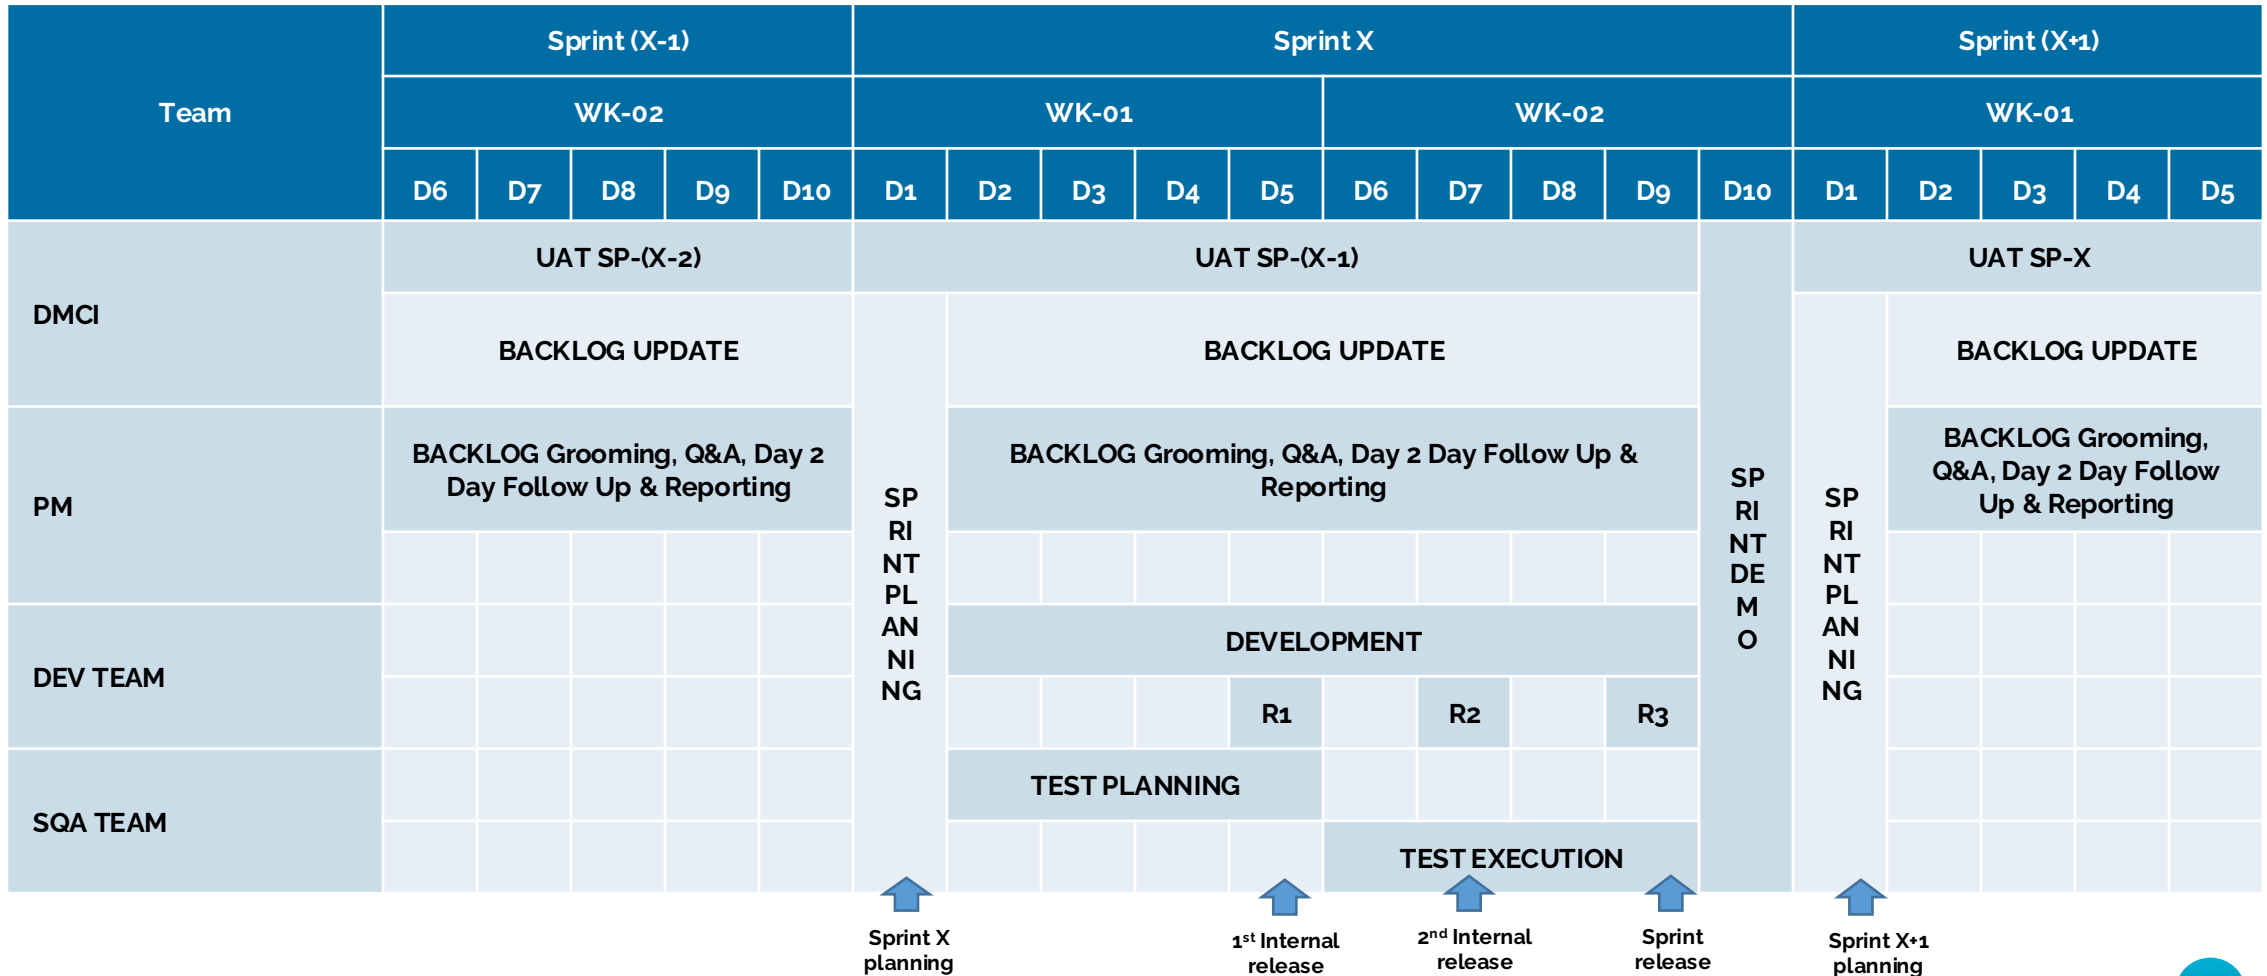

Explanation - Development Method

This method follows an **Agile/Scrum** hybrid approach with clearly defined responsibilities and overlapping phases for efficiency

1. DMCI

- **User Acceptance Testing (UAT):** Conducted at the end of sprints (e.g., UAT for Sprint A in Sprint X-1, UAT for Sprint X in Sprint X)
- **Backlog Updates:** Regularly refine and prioritize the backlog between sprints

2. Project Manager (PM)

- **Sprint Planning:** Defines tasks and goals at the start of each sprint
- **Backlog Grooming:** Ensures backlog items are well-defined and ready for development
- **Day-to-Day Management:** Updates project status and generates reports for tracking progress
- **Sprint Release:** Ensure sprint deliverables and quality

3. Development Team

- **Sprint Demo:** Presents completed work to stakeholders at the end of the sprint
- **Development:** Implements features during the sprint
- **Internal Releases (s*):** Deploys builds to development environments for validation


4. SQA Team

- **Test Planning & Execution:** Prepares and runs tests (likely integration/system tests)
- **Test Reporting:** Prepare test report after test execution


Key Workflow

- **Overlapping Sprints:** Testing (UAT) for one sprint happens while the next sprint is being planned and executed
- **Continuous Backlog Refinement:** All roles contribute to keeping the backlog updated
- **Regular Deliverables:** Internal releases and demos ensure iterative progress

Proposed Engineering Review Process

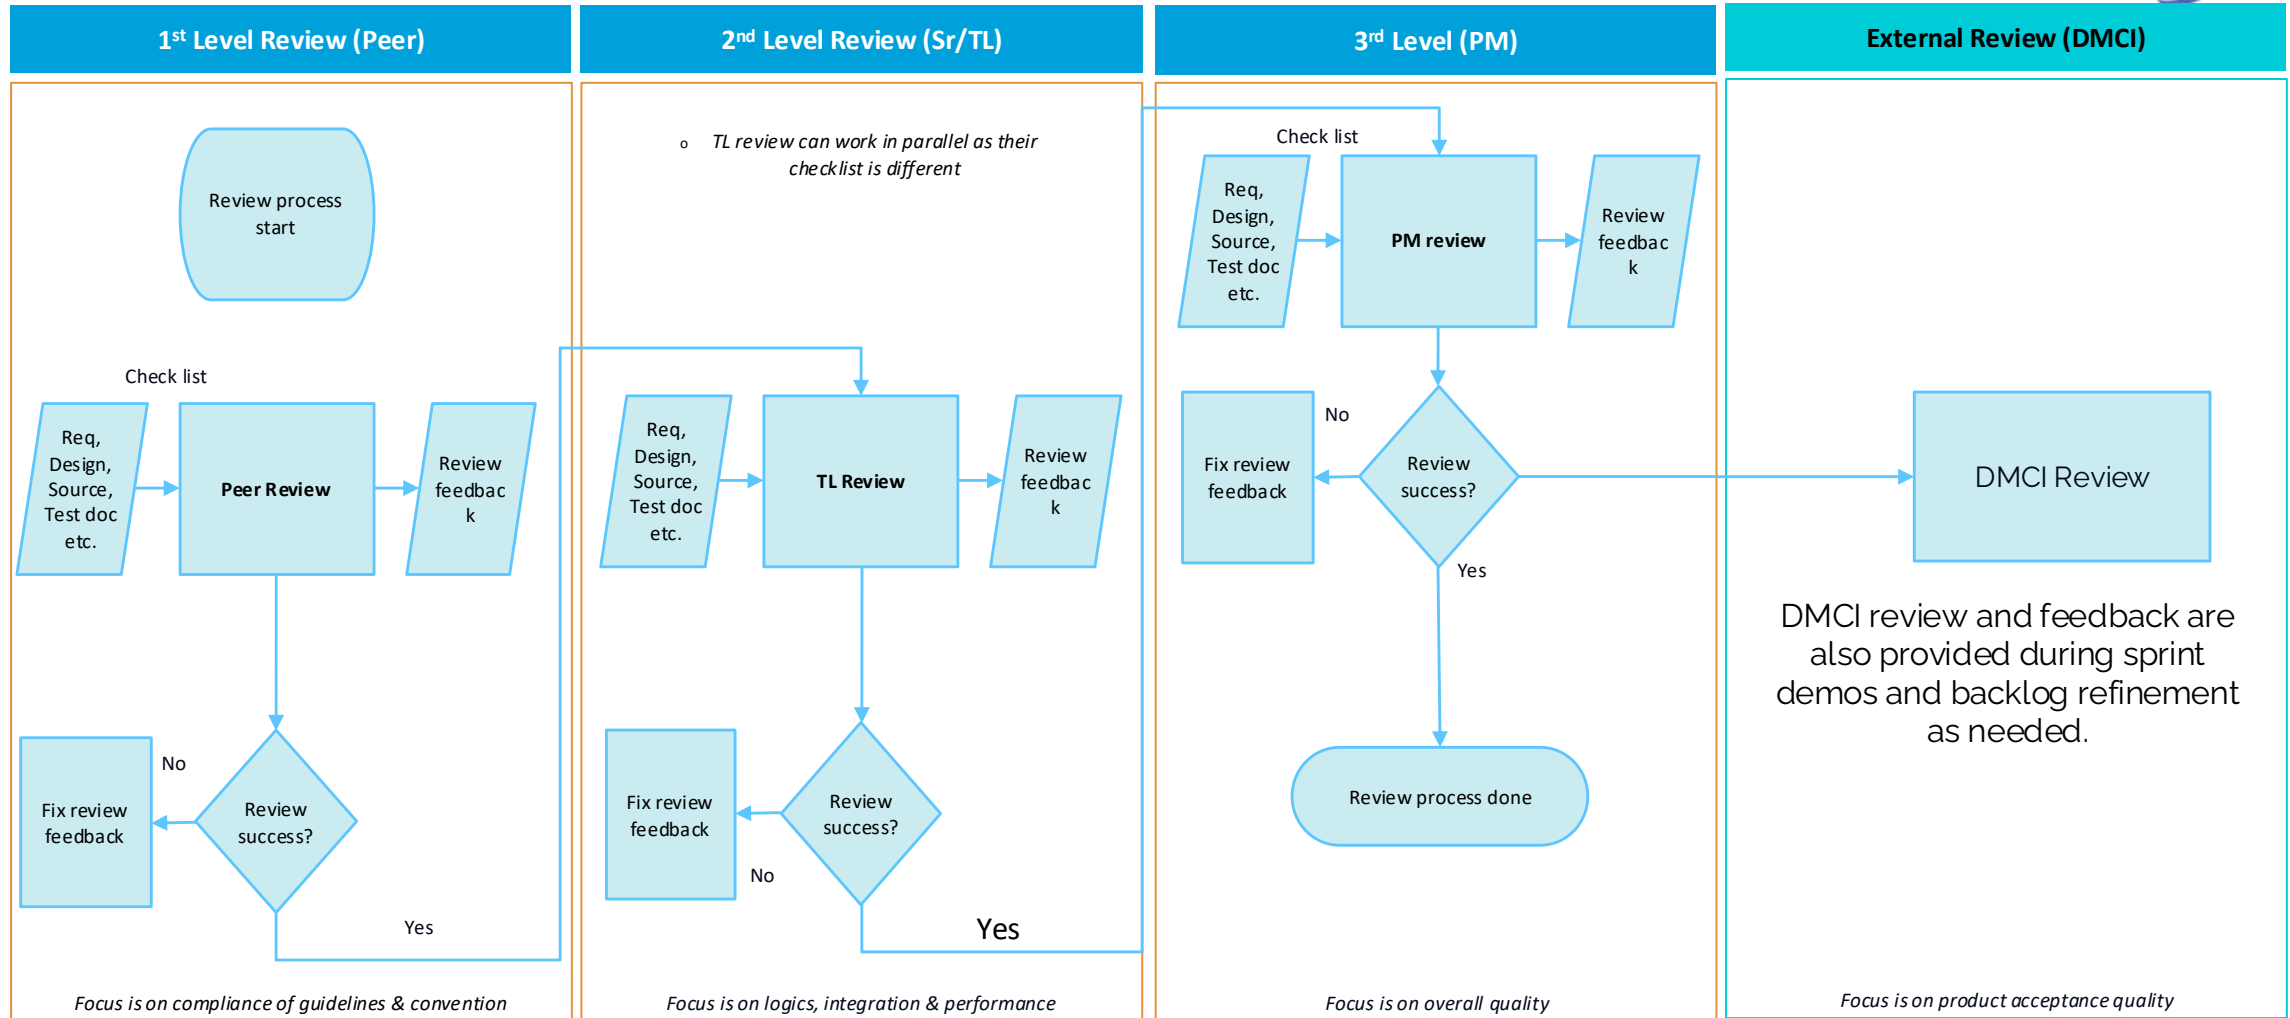

Proposed UI/UX Design Process

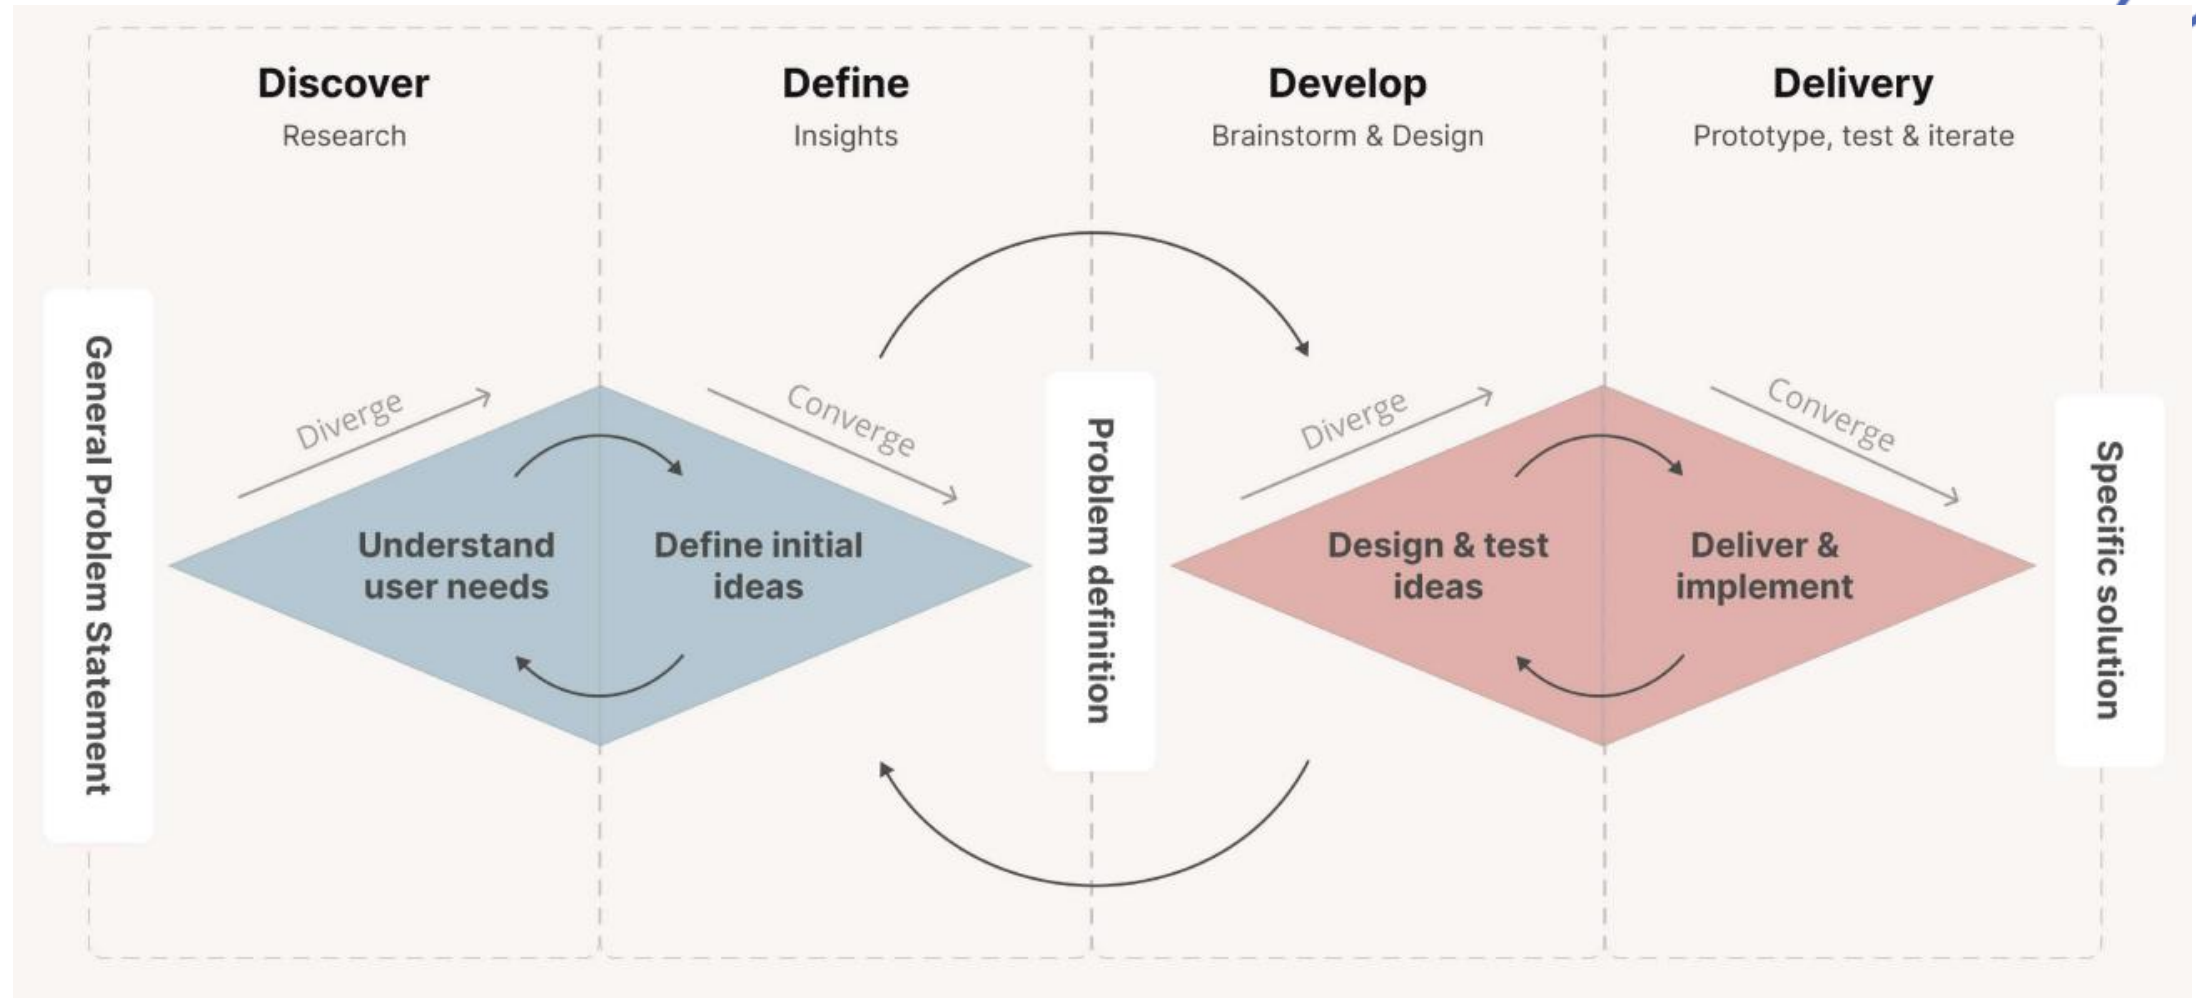

Note: A UI/UX Review will be conducted after project kickoff to confirm design direction and usability with DMCI prior to development. Findings from this sprint will be reflected in subsequent development sprints

Quality Metrics Followed at BJIT

RAG Status (sample color status)		Overall	RED/AMBER/GREEN
Schedule	R	Commitment Slippage = No of stories de-scoped (2) / No of Stories planned(8) X 100 <G = less than or equal 10%> <A = less than or equal 15% & greater than 10%> <R = greater than 15%>	
Effort	G	Effort Deviation = ((Actual Effort - Planned Effort) / Planned Effort) X 100 <G = less than or equal +/-10%> <A = less than or equal +/-15% & greater than +/-10%> <R = greater than +/-15%>	
Bug/Defect Density	A	Bug density = #of defects / Size (Story points or effort) X 100 <G = less than or equal 10%> <A = less than or equal 15% & greater than 10%> <R = greater than 15%>	
Test Efficiency	A	Test efficiency = (QA Bugs/Total Bugs(QA Bugs + UAT Bugs)) x 100 <G = equal to 100%> <A = greater than or equal 90% & less than 100%> <R = less than 90%>	
Post Release Defect	G	Post Delivery Defect Rate = #of sprint defects / Size (Story points or effort) X 100 <G = 0%> <A = less than 7% & greater than 0%> <R = greater than or equal to 7%>	
Customer compliance	R	<G = If customer is happy/give positive feedback/appreciate deliverable etc. with deliverables> <A = If customer is concerned/not very happy/negative feedback etc. deliverable etc. with deliverables> <R = If customer is very unhappy/give very negative feedback/reject deliverable etc. with deliverables>	
Risk/issue	G	<G = If there is no risk> <A = If all the risks are minor (impact is not significant) & no possibility of becoming an issue> <R = If the possibility of the risks to become issue is HIGH & the impact is HUGE>	

Explanation of the RAG (Red-Amber-Green)

The RAG report is a visual project management tool used at BJIT to quickly assess project health across multiple quality metrics. **This report can be submitted after each sprint if requested by the client, serving as a transparent and concise status update.** Here's how it works:

RAG Color Coding System

- Green (G):** Indicates acceptable/good performance (on track)
- Amber (A):** Signals caution/warning (needs attention)
- Red (R):** Indicates critical problems (requires immediate action)

Sprint Scenario:

- Sprint Duration:** 2 Weeks
- Team Size:** 6 Developers, 2 QA, 1 PM
- Planned Work:**
 - 10 User Stories (Total: 50 Story Points)
 - Planned Effort: 300 person-hours
- De-scoped Stories:** 2
- Actual Effort:** 330 hours
- Defects Found:** 8
- BJIT-Reported Bugs:** 8
- UAT/PROD Bugs:** 1 (missed in testing)
- Defects in Production:** 1
- Story Points Released:** 40
- Customer Feedback:** Customer reported frustration with delayed features but appreciated bug fixes

Risk/Issue: Third-party payment API latency

RAG Status (based on sprint scenario)	Overall	RED
Schedule	R	Calculation: $(2 \div 10) \times 100 = 20\%$ slippage RAG Status: RED (>20% slippage)
Effort	A	Calculation: $((330 - 300) \div 300) \times 100 = +10\%$ deviation RAG Status: AMBER (10% over budget)
Bug/Defect Density	R	Calculation: $(8 \div 40) \times 100 = 20\%$ defect density RAG Status: RED (>15% density)
Test Efficiency	A	Calculation: $(8/9) \times 100 = 89\%$ RAG Status: AMBER (89% is slightly below 90% threshold)
Post Release Defect	A	Calculation: $(1 \div 40) \times 100 = 2.5\%$ defect rate RAG Status: AMBER (0-7% range)
Customer compliance	A	RAG Status: AMBER (mixed feedback)
Risk/issue	G	RAG Status: GREEN (low impact)

Recommended Actions:

- Investigate root causes of high defects (e.g., requirements gaps, testing gaps)
- Strengthen QA processes
- Conduct root cause analysis for schedule slippage

Deliverable Items

#	Category	Content	Method	Frequency	Date
1	Application	DMCI Account Management Reporting	Hosted on DMCI Azure server (Stage)	- At the end of each sprint - At the end of major milestone	As per schedule
			Hosted on DMCI Azure server environment (Final Release)	At the end of development	
2	Code & Programs	Updated source code (ETL & Power BI)	- Gerrit (BJIT code repository) - Email document attachment (zip formatted)	- At the end of each sprint - At the end of major milestone	
3	Documentation	- User manual - Deployment manual - Architecture diagram - API specification	Email document attachment (zip formatted)	- At the end of each sprint - At the end of major milestone	
4	Quality Assurance	- Test Case - Test Report - Migration Evidence Report	Email document attachment (zip formatted)	- At the end of each sprint - At the end of major milestone	
5	Reporting	Quality Metrics RAG Report	Email document attachment	At the end of each sprint	

Deliverable Details (1/3)

Category	Deliverable Item	Details
Code & Programs	Account Management Reporting	Source code (ETL & Power BI)
Documentation	User manual	Content of User manual • Overview of the PowerBI web application • Intended users (e.g., admin) • System requirements (browser, OS compatibility) • Navigation Guide • Core Features and Functions with screenshot • Reports
	Deployment manual	Content of Deployment manual • Purpose of the document • Overview of the application (ETL, Power BI) and deployment environment • Prerequisites (tools, accounts, permissions) • Environment specifications • Environment Setup Steps • Build and Deployment Process • Post-Deployment Verification • Rollback Procedure • Access and Security
	Architecture diagram	Content of Architecture diagram • Project architecture diagram • architecture diagram ◦ ETL, Database, Storage service, Deployment & infrastructure

Deliverable Details (2/3)

Category	Deliverable Item	Details
Quality Assurance	Test Case Document	Content of Test Case document • Test case list of a feature includes following ◦ Test Case ID ◦ Test Title ◦ Module / Feature ◦ Preconditions ◦ Test Steps ◦ Test Data ◦ Expected Result ◦ Actual Result ◦ Status ◦ Remarks
Quality Assurance	Test Report	Content of Test Report • Test Summary • Project Name • Test Period • Test Environment • Test Type • Test Execution Overview • Test Case Breakdown • Defects & Issues • Test Coverage Summary • Risks & Observations
Reporting	Quality Metrics RAG Report	RAG Report Metrics • Schedule • Effort • Bug/Defect Density • Test Efficiency • Post Release Defect • Customer compliance • Risk/issue

Assumptions, Preconditions & Holiday Calendar

Assumptions



- **Requirements & Reference Documents**

The estimation and schedule are based strictly on the documents provided by DMCI, including:

- Raw Data Extracted for BSL Conso (Folder)
- Sample Processed BSL (Folder)

Any addition, modification, or removal of features or requirements after proposal submission may require a revision of effort, schedule, and cost.

- **Stakeholder Availability**

DMCI business stakeholders, subject matter experts, and IT representatives will be reasonably available for requirement clarifications, design reviews, sprint demos, and UAT sign-offs.

- **Integration Readiness**

Microsoft Dynamics AX, 365 Finance & Operations (D365 F&O) , documentation, and sandbox environments will be available and stable during the integration phase for ETL process.

- **Infrastructure Responsibilities**

DMCI will provision and maintain Development, Staging and Production environments, including network access and security configurations.

- **Browser & Platform Scope**

The application will be accessed via modern desktop browsers only (Chrome, Edge for Windows; Chrome and Safari for macOS). Need to test Power BI desktop application also. Mobile or native app support is out of scope unless explicitly agreed.

- **Security Standards**

Security implementation will follow standard web application security practices, without specialized compliance requirements (e.g., PCI-DSS, ISO 27001) unless specified separately.

Preconditions

Access & Connectivity

- Valid DMCI VPN access (FortiClient) must be provided to the BJIT team
- Access to UAT and integration endpoints must be granted before development and testing phases

Reports & Approval

- Reports, workflows, and arg. diagrams must be reviewed and approved by DMCI before development.
- Change requests after approval may impact timelines and cost
- DMCI shall conduct structured knowledge transfer (KT) sessions for BJIT Developers, covering all Excel formulas, calculation logic, data dependencies, and report-specific business rules used in the existing reports

Risk & Mitigation



Risk	Description	Mitigation
Requirement Changes	Late changes in business rules or workflows may impact delivery timelines	Formal change request and impact assessment process
M. Dynamic D365, AX integration Complexity	Changes or limitations in D365 F&O , Dynamic AX may delay integration	Early technical workshops and sandbox testing
Security Misconfiguration	Improper environment or access configuration may expose vulnerabilities	Secure configuration guidelines and access reviews
Data Integrity Issues	Incomplete or inconsistent master data can affect computations and reports	Early data validation and reconciliation checks
Dependency Delays	Delays in VPN, UAT, or third-party access	Early access requests and escalation procedures

Bangladesh Holiday Calendar (2026)



Date	Day	Holiday
21 February	Saturday	International Mother Language Day
17 March	Tuesday	Shab e-Qadr (Depends on Moon) *
19 March	Thursday	Eid ul-Fitr (Depends on Moon) *
20 March	Friday	Jumuatul Bidah & Eid ul-Fitr (Depends on Moon) *
21 March	Saturday	Eid ul-Fitr (Depends on Moon) *
22 March	Sunday	Eid ul-Fitr (Depends on Moon) *
23 March	Monday	Eid ul-Fitr (Depends on Moon) *
26 March	Thursday	Independence Day
14 April	Tuesday	Bengali New Year
1 May	Friday	May Day & Buddha Purnima
26 May	Tuesday	Eid ul-Adha (Depends on Moon) *
27 May	Wednesday	Eid ul-Adha (Depends on Moon) *
28 May	Thursday	Eid ul-Adha (Depends on Moon) *
29 May	Friday	Eid ul-Adha (Depends on Moon) *
30 May	Saturday	Eid ul-Adha (Depends on Moon) *
31 May	Sunday	Eid ul-Adha (Depends on Moon) *
26 June	Friday	Ashura (Depends on Moon) *
5 August	Wednesday	July Mass Uprising Day
26 August	Wednesday	Eid-e-Milad un-Nabi (Depends on Moon) *

Signatories for DMCI

Signatories for DMCI Project Developers, Inc. (1/2)



Name: ***Mr. Jayson Gallano***

Title: *Senior Manager, Information Technology*

Signature: _____

Date: _____

DMCI Project Developers, Inc. (a.k.a. DMCI HOMES)

DMCI Homes Corporate Center, 1321 Apolinario Street, Bangkal, Makati City, Metro Manila, PH 1233

BJIT Limited

Name: ***Mr. Jan Venturanza***

Title: *Vice-President, Marketing / Customer Care / Information Technology / Learning and Development / Corporate Planning*

Signature: _____

Date: _____

Signatories for DMCI Project Developers, Inc. (2/2)



Name: ***Mr. Alfredo R. Austria***

Title: *Company President*

Signature: _____

Date: _____

DMCI Project Developers, Inc. (a.k.a. DMCI HOMES)

DMCI Homes Corporate Center, 1321 Apolinario Street, Bangkal, Makati City, Metro Manila, PH 1233

Thank you
